

**Camden County Department of Public Works
Division of Engineering
Roadway Improvements along Blackwood Clementon Road
Gloucester Township, Camden County, New Jersey
Progress Report No. 16
November 21, 2022 to November 25, 2022**



Figure 1: Epoxy striping in progress

Work Completed Period of November 25, 2022

- Installed epoxy striping and thermoplastic striping.
- Installed traffic marking thermoplastic symbols.

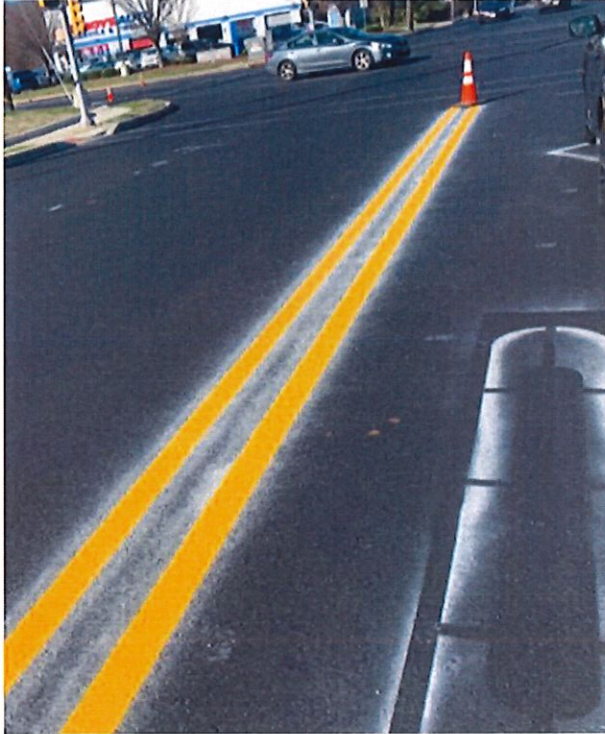


Figure 2: Double yellow epoxy striping

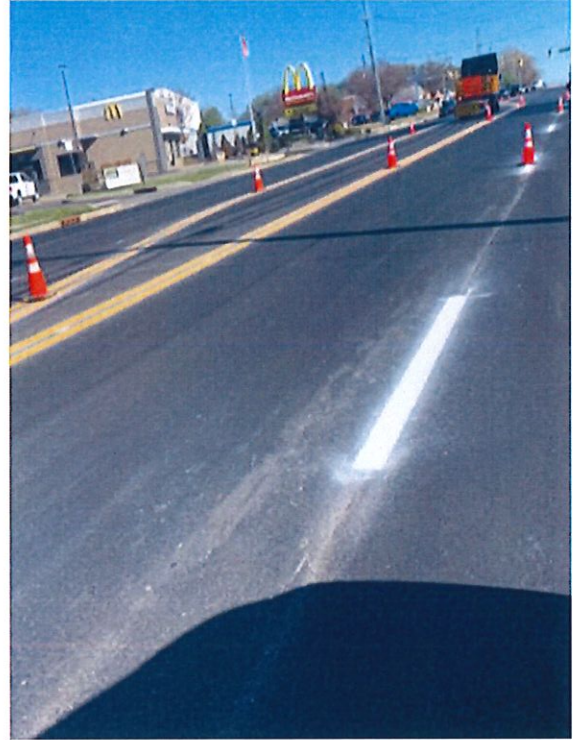


Figure 3: New striping

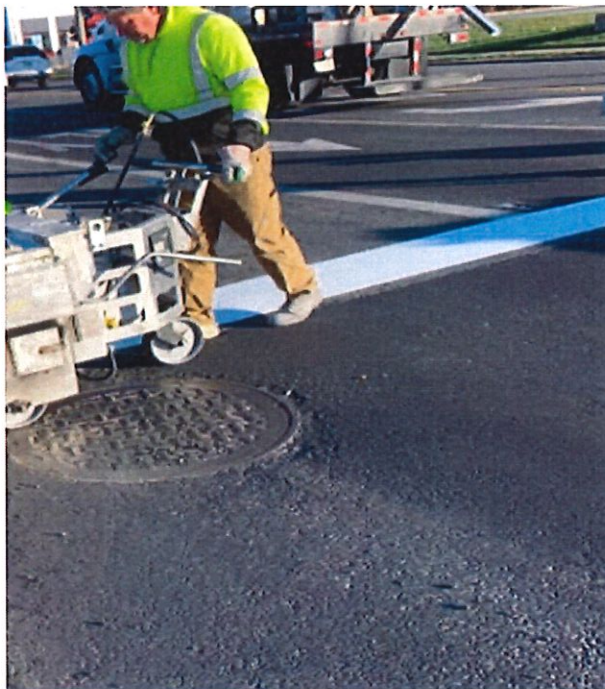


Figure 4: Stop Bar striping



Figure 5: Symbol striping

Quantities Period of November 25, 2022

- **Item #29:** Traffic Stripes, 4" Wide (30,395 LF)
- **Item #30:** Traffic Stripes, 6" Wide (2,488 LF)
- **Item #32:** Traffic Stripes, 24" Wide (860 LF)
- **Item #34:** Traffic Markings Symbols-Right Arrow (31 SF)
- **Item #35:** Traffic Markings Symbols-Only (1,036 SF)

Summary of Work Completed Period of November 25, 2022

- The crew installed 4" epoxy striping and 24" thermoplastic striping. Continued with installing 6" wide, 24" wide and traffic marking thermoplastic symbols.

Anticipated Work for Period of November 28, 2022


- Continue with epoxy and thermoplastic striping.

Notice to Proceed: August 1, 2022

Substantial Completion: October 30, 2022

Final Completion: November 29, 2022

Prepared By:



Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
