

**Camden County Department of Public Works
Division of Engineering
Roadway Improvements along Blackwood Clementon Road
Gloucester Township, Camden County, New Jersey
Progress Report No. 7
September 19, 2022 to September 23, 2022**



Figure 1: Inlet reconstruction area restored

Work Completed Period of August 26, 2022

- 18" RCP removal and replacement.
- Backfilling trench, DGA added, HMA installed.
- Reconstruction of inlets and new curb pieces installed.



Figure 2: Compacting DGA



Figure 3: Section of RCP



Figure 4: Installing DGA

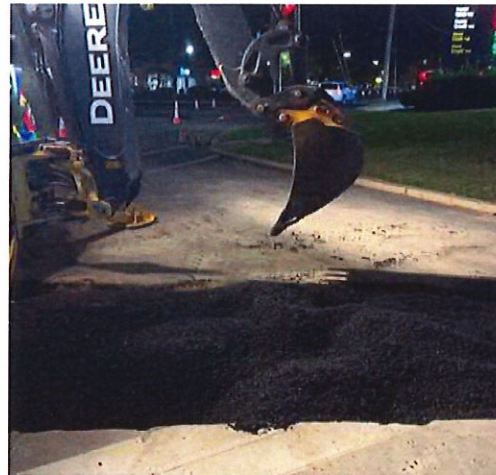


Figure 5: Installing HMA

Quantities Period of August 26, 2022

- **Item #8:** Traffic Safety Services (58.50 MH)
- **Item #14:** HMA Base Course, 19M64, 6" Thick (9.53 TONS)
- **Item #21:** Type N-Eco Curb Piece (4 Units)
- **Item #23:** Reconstruct Inlet, Type B Using New Casting (4 Units)
- **Item S-1:** Reinforced Concrete Pipe, 18" (40 LF)

Summary of Work Completed Period of August 26, 2022

- The crew completed inlet reconstructions and installed new Type N Echo curb pieces. Crew removed existing RCP and replaced with 18" RCP. Continued with backfilling trench, added and compacted DGA, and installed HMA.

Anticipated Work for Period of August 29, 2022


- Concrete work and electrical work on site.

Notice to Proceed: August 1, 2022

Substantial Completion: October 30, 2022

Final Completion: November 29, 2022

Prepared By:



Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
