

**Camden County Department of Public Works
Division of Engineering
Roadway Reconstruction and Traffic Signal Improvements
to Route 70 Feeder – 27th Street (CR 601) to Federal Street (CR 537)
City of Camden, Camden County, New Jersey
Contract Bid - B6-23
Progress Report No. 01
September 4, 2023 to September 15, 2022**



Figure 1: Concrete Sidewalk

Work Completed Period of September 15, 2023

- Installed sidewalk and curb forms and finished new concrete curb and sidewalk.
- Reset sanitary sewer cleanout, water meter, water valve, and gas valve boxes.
- Removal of trees.



Figure 2: Concrete Curb and Sidewalk



Figure 3: Forming Concrete Curb



Figure 4: Reset Sewer Cleanouts

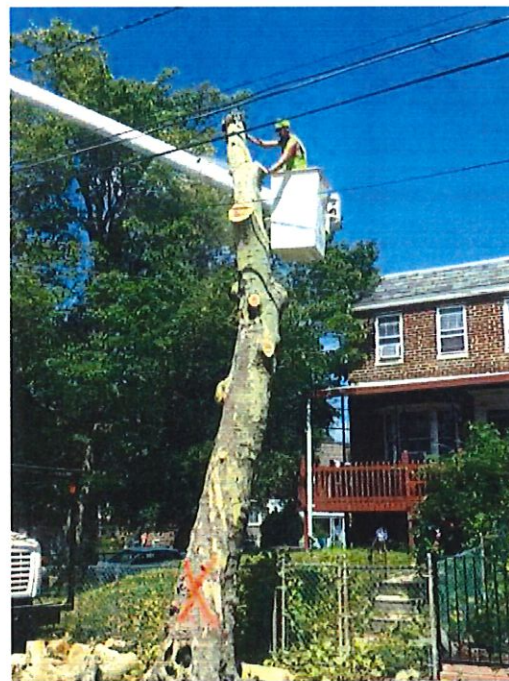


Figure 5: Tree Removal

Quantities Period of September 15, 2023

- **Item #7:** Inlet Filter Type 2, 2' x 4' (14.00 UN)
- **Item #42:** Concrete Sidewalk, 5" Thick (346.72 SY)
- **Item #46:** 8" x 6" x 18" Concrete Vertical Curb (673.00 LF)
- **Item #54:** Reset Water Meter Box (13.00 UN)
- **Item #55:** Reset Water Valve Box (2.00 UN)
- **Item #57:** Reset Sanitary Sewer Cleanout (12.00 UN)
- **Item #60:** Reset Gas Valve Box (1.00 UN)
- **Item #81:** Tree Removal, Over 24" to 30" Diameter (9.00 UN)
- **Item #87:** Police Traffic Director (57.50 HR)

Summary of Work Completed Period of September 15, 2023

- Contractor began with removing existing concrete curb and sidewalk along 27th Street between Berkley Street and Line Street. Forms were then installed at the removed sections and new concrete curb and sidewalk was then poured and finished. Sanitary sewer cleanouts, gas valves, water valves and water meter boxes were also reset within those limits. Police traffic directors were utilized during the days work for traffic control safety measures.

Anticipated Work for Period of September 29, 2022

- Continuation of concrete work.

Notice to Proceed: September 5, 2023

Substantial Completion: February 11, 2024

Final Completion: March 2, 2023

Prepared By:

Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
