

**Camden County Department of Public Works
Division of Engineering
Roadway Reconstruction and Traffic Signal Improvements
to Route 70 Feeder – 27th Street (CR 601) to Federal Street (CR 537)
City of Camden, Camden County, New Jersey
Contract Bid - B6-23
Progress Report No. 06
November 13, 2023 to November 24, 2023**

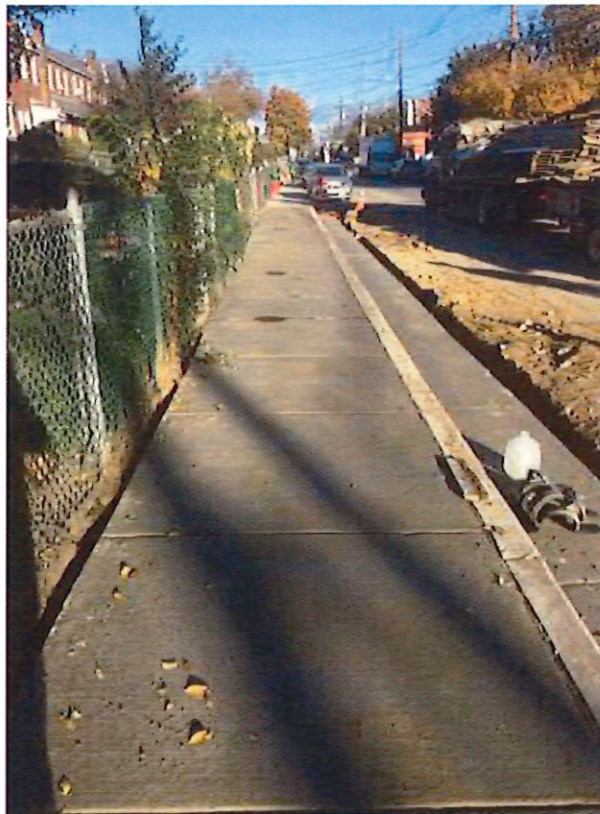


Figure 1: Concrete Sidewalk & Curb

Work Completed Period of November 24, 2023

- Forming and finishing new concrete curb, sidewalk, ADA compliant curb ramps and driveways. Installation of new brick pavers were also completed.
- Continuing traffic signalization installation. (Installment of Traffic Signal Foundations)
- Reset sanitary sewer cleanouts and water meter boxes.
- Topsoiling and seeding restoration.



Figure 2: ADA Compliant Curb Ramp



Figure 3: Traffic Signal Foundation



Figure 4: ADA Ramp and Brick Pavers

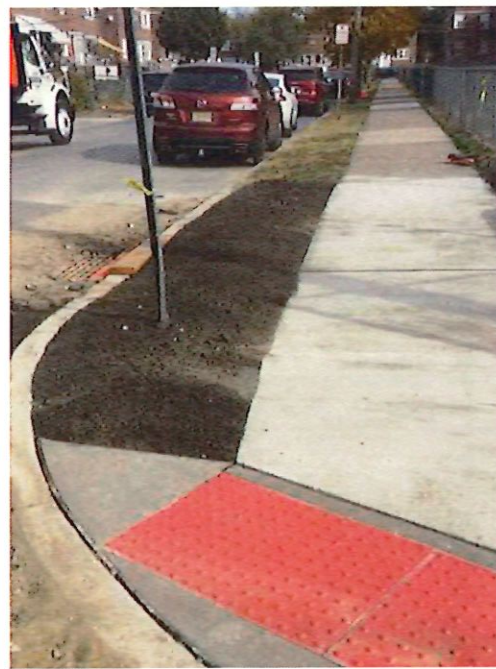


Figure 5: Topsoil & Seeding

Quantities Period of November 24, 2023

- **Item #15:** Traffic Control Truck with Mounted Crash Cushion (1.00 UN)
- **Item #42:** Concrete Sidewalk, 5" Thick (379.55 SY)
- **Item #43:** Brick Pavers (25.09 SY)
- **Item #44:** Concrete Driveway, 6" Thick (18.77 SY)
- **Item #45:** Detectable Warning Surface (17.57 SY)
- **Item #46:** 8" x 6" x 18" Concrete Vertical Curb (281.50 LF)
- **Item #51:** Monolithic Concrete Curb And Gutter (79.00 LF)
- **Item #54:** Reset Water Meter Box (15.00 UN)
- **Item #57:** Reset Sanitary Sewer Cleanout (18.00 UN)
- **Item #63:** Foundation, Type SFT (3.00 UN)
- **Item #65:** Foundation, Type SPF (1.00+ UN)
- **Item #82:** Topsoil Spreading, 5" Thick (115.82 SY)
- **Item #84:** Fertilizing and Seeding, Type, A-3 (115.82 SY)

Summary of Work Completed Period of November 24, 2023

- Contractor began with removing existing concrete curb, sidewalk, and driveways along 27th Street between the Marlton Pike and Berkley Street. Forms were then installed at the removed sections and new concrete curb, sidewalk, ADA compliant ramps, and driveways were then poured and finished. Sanitary sewer cleanouts and water meter boxes were also reset within those limits. Traffic signalization improvements continued this period at the intersection of Berkley Street and 27th Street with the installation of traffic signal foundations. Restoration began this period with the contractor placing topsoil and seeding down in damaged areas throughout the project limits. Advanced warning signs, VMS boards, traffic control mounted crash trucks, breakaway barricades, and cones were utilized in setting up a detour for traffic control safety measures during this period of work.

Anticipated Work for Period of December 8, 2023


- Continuation of concrete work, drainage work, traffic signalization improvements and start of roadway boxout.

Notice to Proceed: September 5, 2023

Substantial Completion: February 11, 2024

Final Completion: March 2, 2024

Prepared By:


Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
