

**Camden County Department of Public Works
Division of Engineering
Roadway Improvements along Blackwood Clementon Road
Gloucester Township, Camden County, New Jersey
Progress Report No. 8
September 26, 2022 to September 30, 2022**



Figure 1: Pedestal formwork

Work Completed Period of September 30, 2022

- Push button pedestal foundation work on site.



Figure 2: Excavating for pedestal foundation

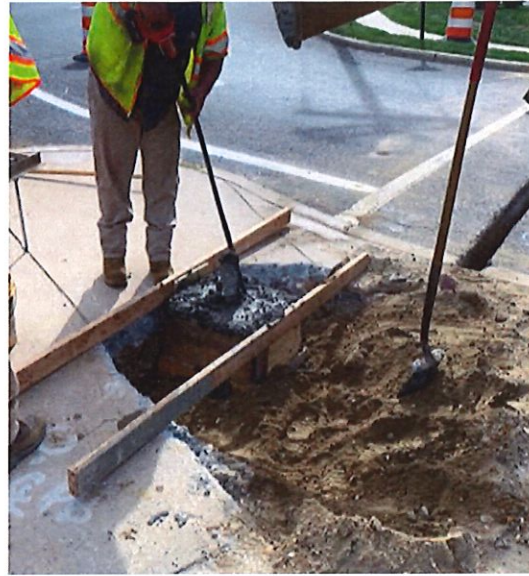


Figure 3: Pouring pedestal foundation



Figure 4: Roadway trench

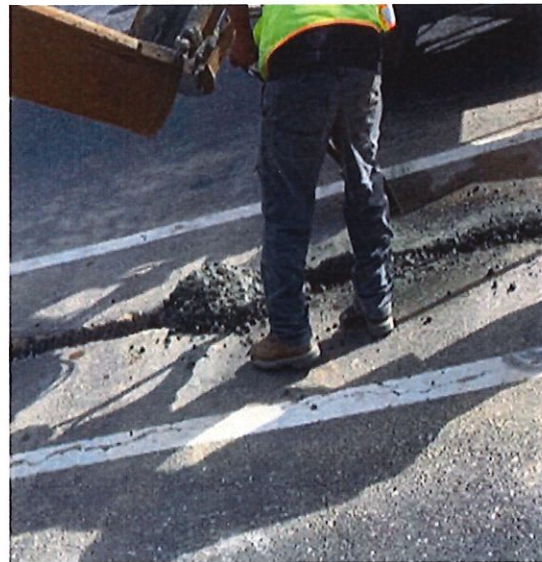


Figure 5: Filling trench with concrete

Quantities Period of September 30, 2022

- **Item #8:** Traffic Safety Services (24.50 MH)

Summary of Work Completed Period of September 30, 2022

- The crew removed small sections of concrete in the island at the intersection. The crew completed excavating, digging, and forming for electrical pedestal foundation.

Anticipated Work for Period of October 3, 2022

- Concrete work on site.

Notice to Proceed: August 1, 2022

Substantial Completion: October 30, 2022

Final Completion: November 29, 2022

Prepared By:

Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
