

Department of Public Works

Susan Shin Angulo
Freeholder Liaison

John Wolick
Director



Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com




Clementon-Berlin Road (CR 534) Bridge over North Branch of Timber Creek Structure No. 048E006

Borough of Clementon
County of Camden, NJ
Weekly Progress Report #12
December 24 to December 28




After the concrete was poured blankets were installed and heat to meet the requirements of the specs

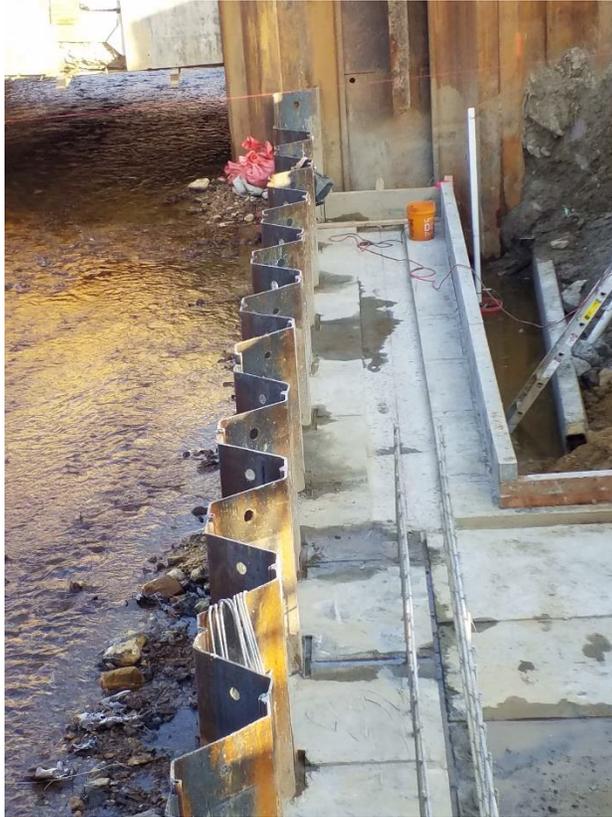

East footing once cured and ready for placement of the culverts.



First section lifted off truck that was in roadway

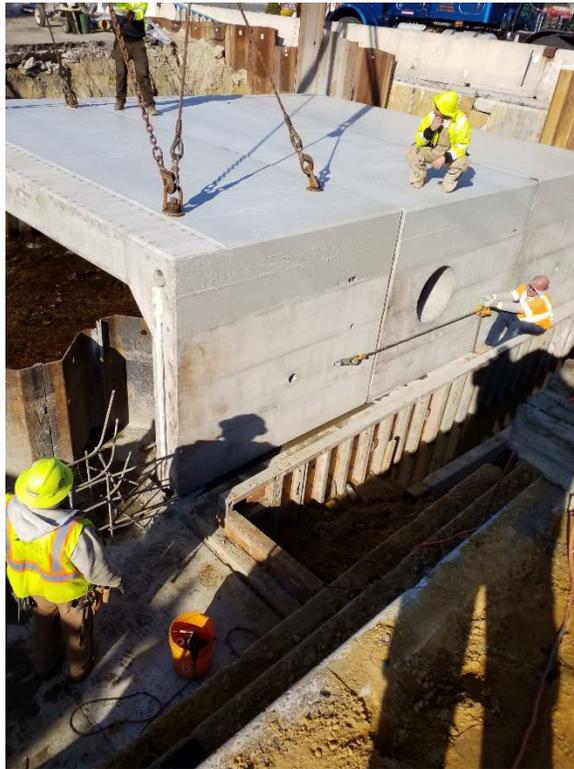

Last section in this stage placed and set into place.



Post tensioning machine to apply the correct kips to the strands

Partial NTP : August 15, 2018
NTP : September 20, 2018

Contractor Duration: 512 days
Completion date February 14, 2020

19.3% of time used to date

32.9% paid to date

The Notice to Proceed was given on September 20, 2018. Contractor has the duration of 512 day making the completion date on February 14, 2020.

As per plan the footings were poured and cured using heat and blankets. On December 27th the 3 sections of the culvert were delivered set into place. Traffic was detoured by recommendation of the local police. The operation took just over 2 hours. Then the roadway was reopened. Once the 3 sections were place the post tension strands were installed and tensioned. Grouting of the strands and base will take place next week.

The contractor will be starting to place forms for the wingwalls and working on the roadway items of the project.

Prepared by: Tony Guerrieri, AECOM Project Manager
