

Department of Public Works

Susan Shin Angulo  
Freeholder Liaison

John Wolick  
Director



Making It Better, Together.

Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988  
[highway@camdencounty.com](mailto:highway@camdencounty.com)




**Clementon-Berlin Road (CR 534) Bridge over  
North Branch of Timber Creek Structure No. 048E006**

Borough of Clementon  
County of Camden, NJ  
Weekly Progress Report #13  
December 31 to January 4, 2019



Photo showing the Pre-cast culvert in place looking for the east side

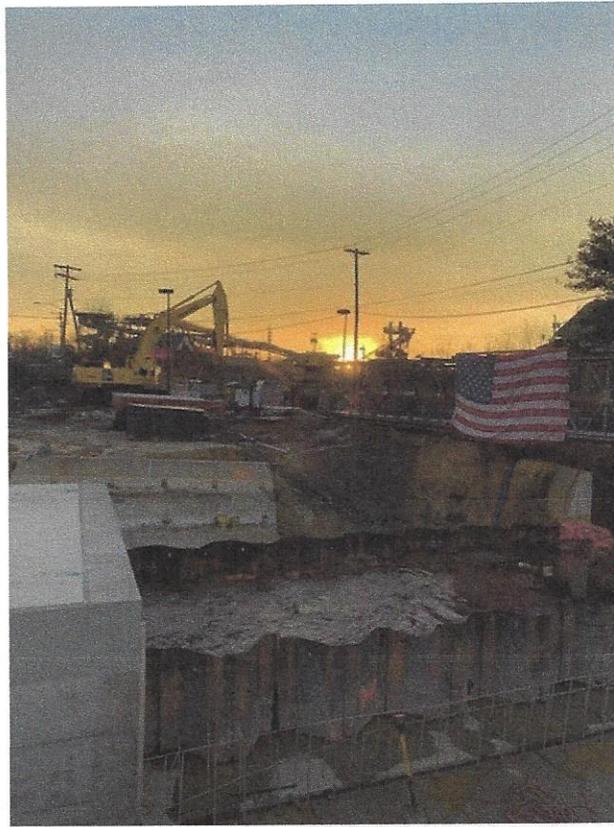

This is the last sun-rise of 2018 with culvert in place and Flag on Pedestrian Bridge



Wingwall form going up and I-9 being installed on Eat side.



I-9 being compacted as in is being placed



West side of structure will follow after east side is completed.

Partial NTP : August 15, 2018  
NTP : September 20, 2018

Contractor Duration: 512 days  
Completion date February 14, 2020

20.7% of time used to date

50.9% paid to date

The Notice to Proceed was given on September 20, 2018. Contractor has the duration of 512 day making the completion date on February 14, 2020.

Three sections of the culvert were placed the week of December 24<sup>th</sup>. The week of December 31<sup>st</sup> the sections were grouted in and work began on East side Wingwall forms. I-9 is being placed and compacted as per specifications.

The contractor will continue on forming the pouring wingwalls after which they will move to working on the roadway in this stage.

**Prepared by:** Tony Guerrieri, AECOM Project Manager
