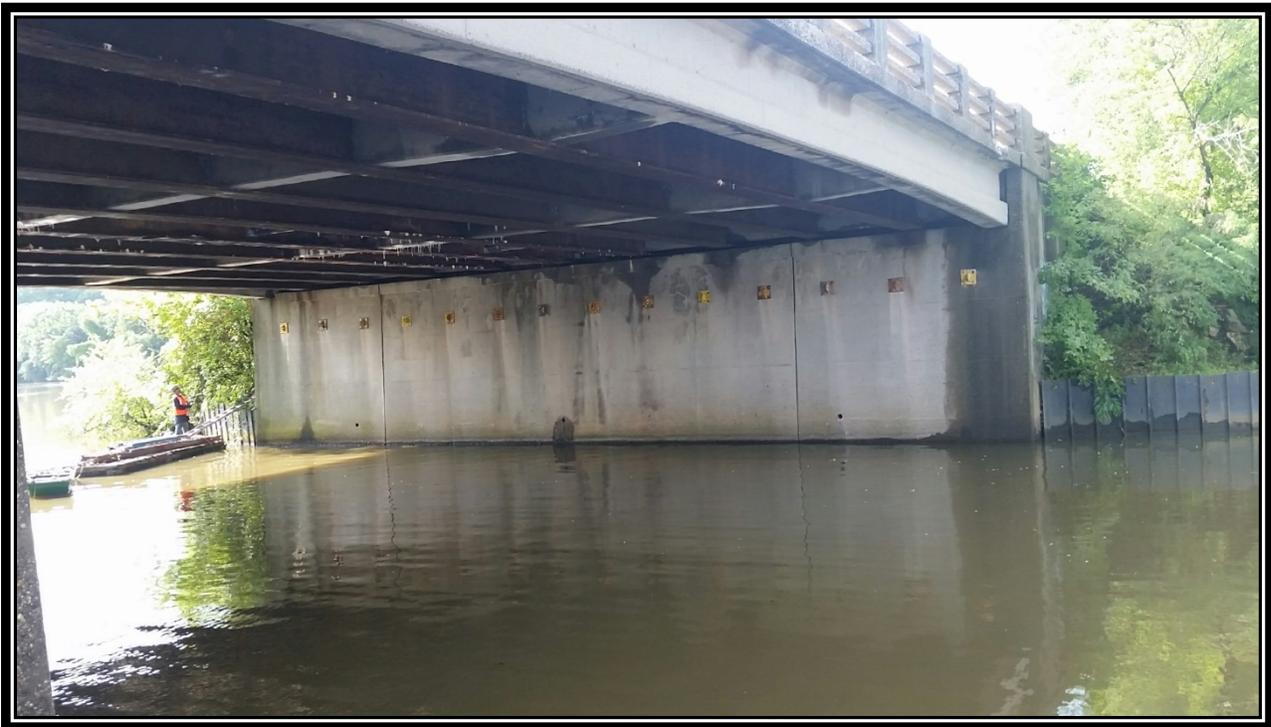


**Camden County Department of Public Works  
Division of Engineering  
Superstructure Repairs for Cuthbert Boulevard (CR 636) Bridge and  
Grove Street (CR 644) Bridge over Cooper River  
Camden County, New Jersey  
Weekly Progress Report No. 1  
July 30, 2018 to August 4, 2018**



*Figure 1: Cuthbert Blvd - Shielding Setup – 8/1/18*

**Work Completed Week of July 30, 2018**

- Grove Bridge
  - MPT Setup for detour (covered)
- Cuthbert Bridge
  - Receiving shielding materials
  - Erecting shielding

**Superstructure Repairs for Cuthbert Boulevard (CR 636) Bridge  
and Grove Street (CR 644) Bridge over Cooper River**

**Camden County, New Jersey**

**Weekly Progress Report No. 1: 7/30/18-8/4/18**

**Quantities Week of July 30, 2018**

- **Item 10** – Pollution Control System – In Progress
- **Item 13** – Police Uniform Law Enforcement Officer – 4 Hours

**Summary of Work Completed Week of July 30, 2018**

South State Inc. (SSI) employed their subcontractor, Allied Painting Inc (API) to install shielding starting at Cuthbert Blvd. The contractor installed the shielding and work platform per the approved shop drawing. The metal decking was hung by cables from the concrete deck.

No work has begun at Grove Street.

**Anticipated Work for Week of August 6th, 2018**

SSI subcontractor API will complete shielding installation at Cuthbert Bridge. API will begin blasting and priming of steel superstructure. Crew will mobilize to Grove Street to begin erection of shielding. This work will not require the detour to be implemented.

**Notice to Proceed**

July 16, 2018

**Contract Completion**

Substantial Completion      March 27, 2018

Final Completion              April 26, 2019

Prepared By:

Joseph R. Ragusa, P.E.  
Construction Manager  
Remington and Vernick Engineers
