

Department of Public Works

Susan Shin Angulo
Freeholder Liaison

John Wolick
Director




Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com




Clementon-Berlin Road (CR 534) Bridge over North Branch of Timber Creek Structure No. 048E006


Borough of Clementon
County of Camden, NJ
Weekly Progress Report #29
May 6 to May 10, 2019

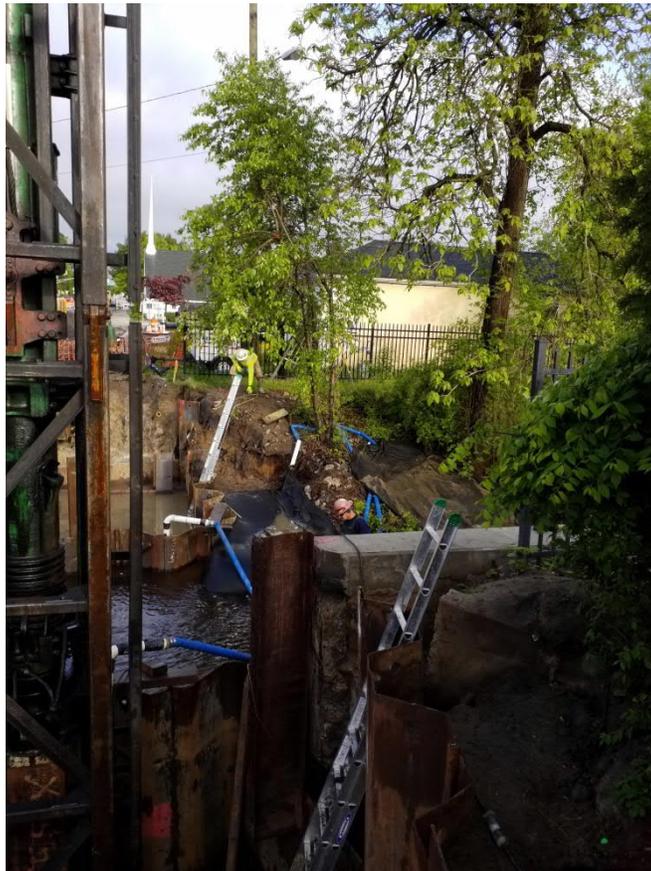


Pile driving operation continues.

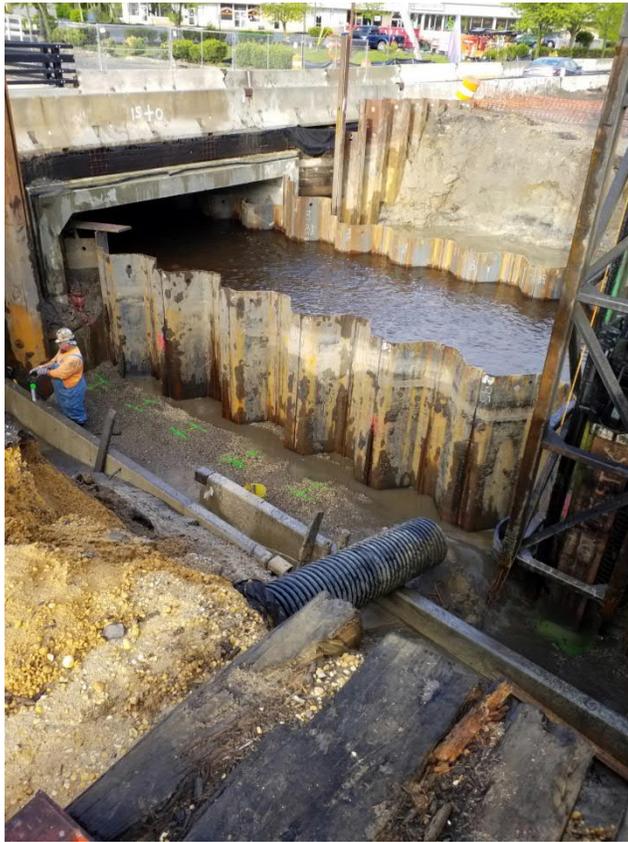

Mark out for the piling.

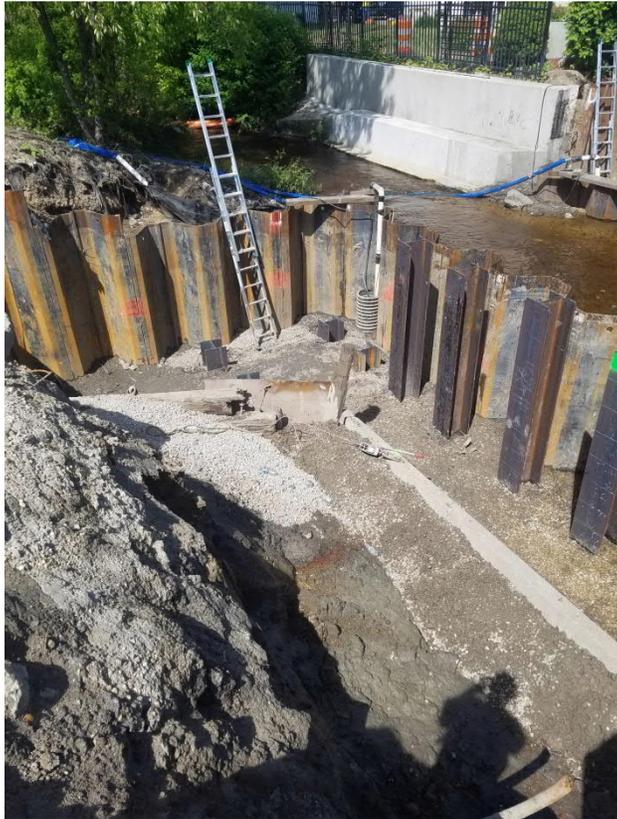

Piles driven.

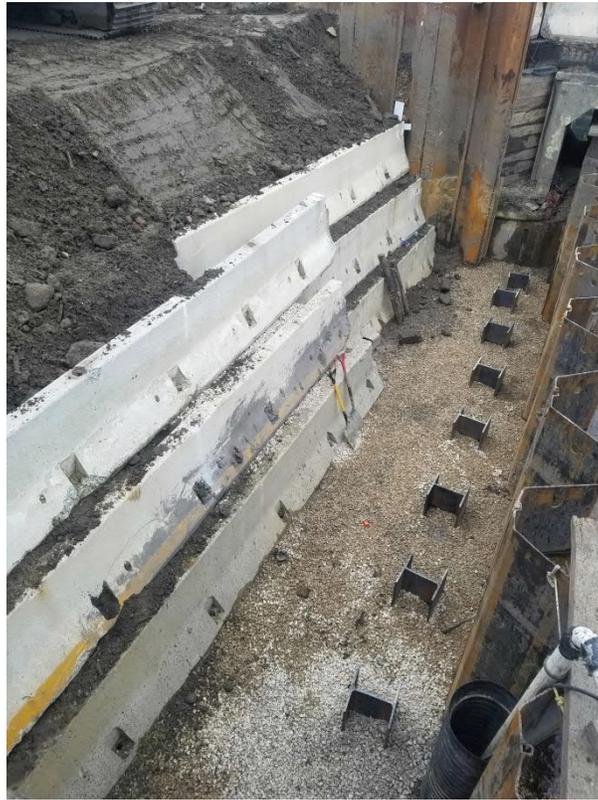

Piles cut off at required elevation.



Building forms to pour concrete footings.

Partial NTP : August 15, 2018
NTP : September 20, 2018

Contractor Duration: 512 days
Completion date February 14, 2020

45.3 % of time used to date

69.4 % paid to date

The Notice to Proceed was given on September 20, 2018. Contractor has the duration of 512 day making the completion date on February 14, 2020.

The contractor has completed the installation of the piling on both the North East and West side of the North Branch of Timber Creek and has started building the forms for the concrete footings.

Prepared by: Tony Guerrieri, Jim Carrigan, AECOM
