


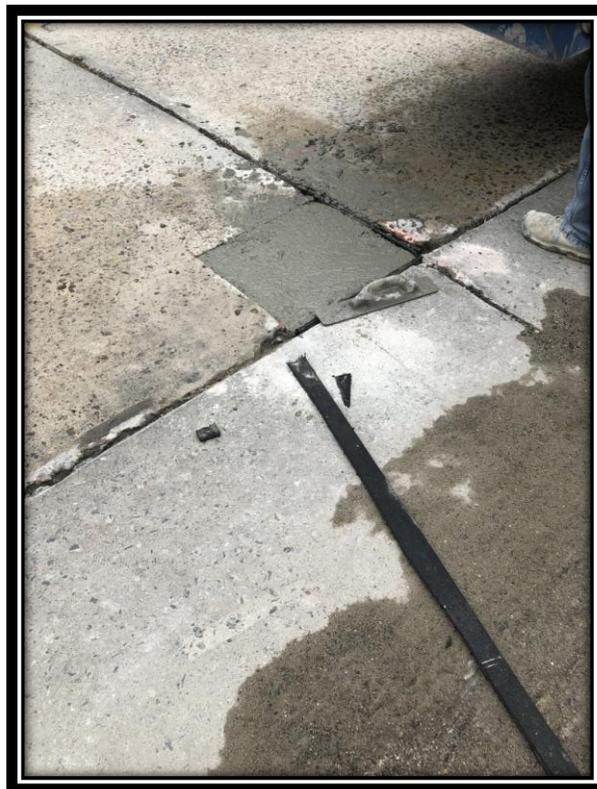

**ERIAL-CLEMENTON ROAD (CR 703)  
RECONSTRUCTION PROJECT – PHASE I  
ERIAL-NEW BROOKLYN ROAD (CR 706) TO TURNSEVILLE-HICKSTOWN ROAD (CR  
688) AND THE VICINITY OF CLOVERDALE AVENUE  
ERI Job # 30750 44  
Township of Gloucester and Borough of Pine Hill  
County of Camden, New Jersey**

**WEEKLY PROGRESS REPORT #14  
May 7, 2018 to May 11, 2018**



*Figure: 1 – Installation of partial depth concrete slab repair along the southbound lane between Turnersville - Hickstown Road and Bromley Drive*



*Figure: 2 – Inlet reconstruction including a new casting along the southbound lane between Bromley Drive and Shultz Avenue*



*Figure: 3 – Removal of existing concrete slab in preparation of full depth concrete slab repair along the southbound lane between Bromley Drive and Shultz Avenue*

**Work Completed the Week of May 7, 2018:**

South State, Inc's concrete crew completed the inlet repair in the Gloucester Township portion of the project. South State reset 1 inlet with the existing casting, reset 2 inlets using new castings, and reconstructed 5 inlets using new castings. The concrete crew then completed the remaining full depth concrete slab repairs adjacent to the newly repaired inlets. The concrete crew poured 67.5 SY of full depth concrete repair with class V concrete mix along both the northbound and southbound lanes between Hickstown – Turnersville Road and Erial – New Brooklyn Road. The entire full depth slab repair is now complete. South State then began the partial depth concrete slab repairs in the southbound lane between Hickstown – Turnersville Road and Erial – New Brooklyn Road. The concrete crew poured 30.72 SY of full depth concrete repair

- #16: Police Uniform Law Enforcement Officer – 80 Hours**
- #32: Partial Depth Concrete Repair – 30.72 SY**
- #33: Full Depth Concrete Repair, Concrete Class V – 67.5 SY**
- #40: Reset Existing Casting – 1 Unit**
- #S2: Reset Inlet Using New Casting – 2 Units**
- #S3: Reconstruct Inlet Using New Casting – 5 Units**

**Anticipated Work for the Week of May 14, 2018:**

South State's concrete crew will complete the partial depth repairs in the Gloucester Township portion of the project.

**Spring Notice to Proceed Date: April 16, 2018**

**Anticipated Completion Date: June 29, 2018**

Prepared By:



C. Jeremy Noll, PE, CME  
Resident Engineer  
Environmental Resolutions, Inc.
