

Department of Public Works

Susan Shin Angulo  
Freeholder Liaison

John Wolick  
Director



Making It Better, Together.

Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988  
[highway@camdencounty.com](mailto:highway@camdencounty.com)




## Clementon-Berlin Road (CR 534) Bridge over North Branch of Timber Creek Structure No. 048E006


Borough of Clementon  
County of Camden, NJ  
Weekly Progress Report #31  
May 20 to May 24, 2019



Forms removed from North East footing.  
Studs welded to sheeting.

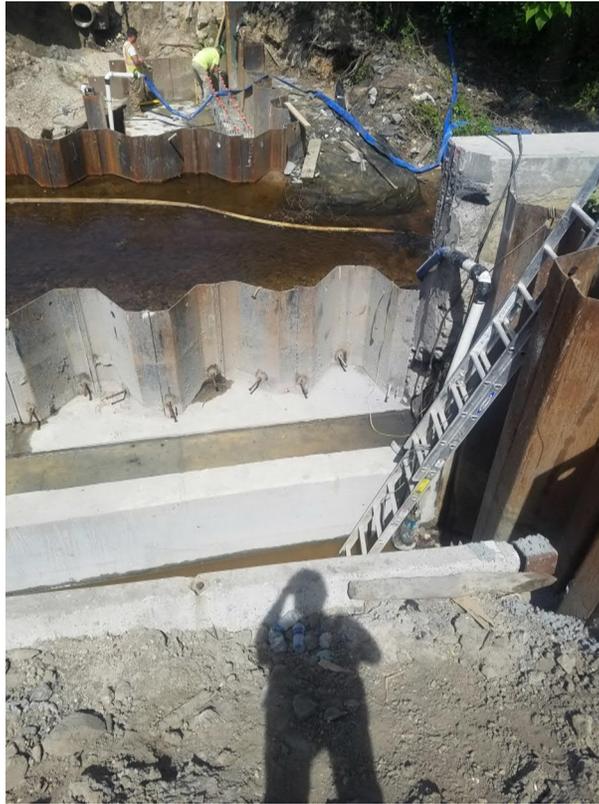

Forms removed from North West footing.  
Studs welded to sheeting

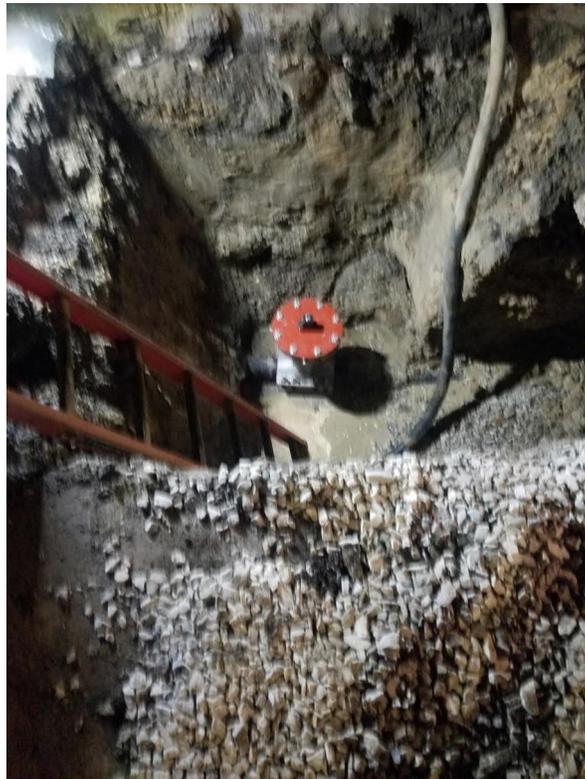

Water main break, new valve installed.

Partial NTP : August 15, 2018  
NTP : September 20, 2018

Contractor Duration: 512 days  
Completion date February 14, 2020

48.0 % of time used to date

69.4 % paid to date

The Notice to Proceed was given on September 20, 2018. Contractor has the duration of 512 days making the completion date on February 14, 2020.

The contractor has removed forms from both the North East and West side footings. Steel studs were welded to sheeting that will be encased in concrete at a later date. Contractor did not work Wednesday – Friday due to the availability of their crane needed to set the culverts.

There was a water main break on Friday afternoon and Clementon water/sewer responded. Clementon contacted Garrison contractor to install new water valve. MidLantic called in to relocate their equipment to allow Garrison access to the area with their equipment.

Prepared by: Tony Guerrieri, Jim Carrigan, AECOM
