

**Camden County Department of Public Works
Division of Engineering
Roadway & Drainage Improvements along Fern Avenue (CR 640)
Haddon Ave (CR 561) to Cuthbert Boulevard (CR 636)
Camden County, New Jersey
Weekly Progress Report No. 10
June 24, 2019 to June 30, 2019**

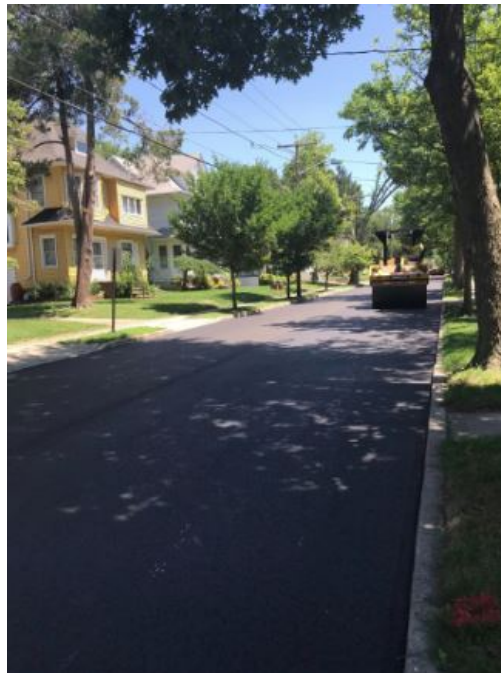


Figure 1: Top paving along Fern Ave

Work Completed Week of June 24, 2019

- Base paving from Burrwood Ave to Cuthbert Boulevard
- Top paving from Cuthbert Boulevard to Haddon Ave

Quantities Week of June 24, 2019

- **Item #7:** Police Uniform Law Enforcement Officer (48 MH)
- **Item #17:** Hot Mix Asphalt 19M64 Base Course, 2" Thick (541.81 TON)
- **Item #18:** Hot Mix Asphalt 9.5M64 Surface Course, 2" Thick (1187.65 TON)
- **Item #19:** Tack Coat (If & Where Directed) (577 GAL)

Summary of Work Completed Week of June 24, 2019

Asphalt Paving Systems (APS) completed the base and top paving operations on Fern Ave from Cuthbert Boulevard to Haddon Ave. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Police Uniform Law Enforcement Officers are additionally utilized for traffic control. An onsite progress meeting was held on June 25, 2019 to review all project related activities.

Anticipated Work for Week of July 1, 2019

APS will continue restoration work and install roadway signage along Fern Ave, possible concrete work at the intersection with Haddon Ave. HMA cores will be taken by the testing agency. Daily traffic control will continue to be implemented for the duration of the project.



Figure 2: Base paving operations



Figure 3: Top paving at Cuthbert Boulevard intersection



Figure 4: Top paving at Burrwood Ave intersection



Figure 5: Top paving along Fern Ave

Notice to Proceed

April 22, 2019

Contract Completion

Substantial Completion

July 21, 2019

Final Completion

August 20, 2019

Prepared By:

Joseph R. Ragusa, P.E.

Remington and Vernick Engineers
