



Berlin-Cross Keys Road Improvement Project Contract 1
Boroughs of Berlin and Pine Hill and Township of Winslow, Camden County, New Jersey
Camden County
Bid No. B9-19

Maser Consulting Project No 19002364G

Progress Report #10
Friday, January 10, 2020



Figure 1: Contractor installing the REDI-ROCK cap block on the west retaining wall.



Figure 2: Crew completed the west REDI-ROCK retaining wall.

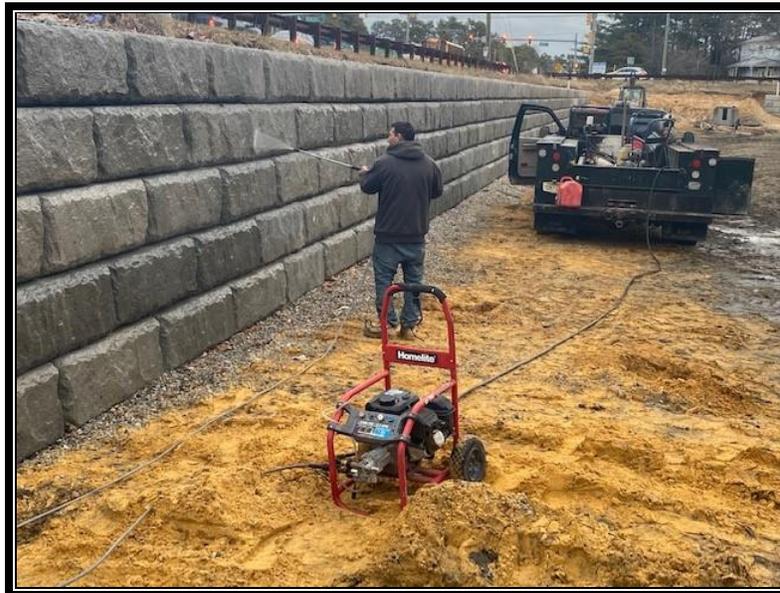


Figure 3: Contractor power-washing the REDI-ROCK retaining wall.



- **CONTRACT ITEMS COMPLETED THIS WEEK**
 - Item No.16 Retaining Wall 1,389 S.F.

- **ITEMS COMPLETED THIS PAST WEEK**
 - Sub-contractor completed the west REDI-ROCK retaining wall.
 - Sub-contractor installed the under-drain pipe for the west retaining wall.
 - Crew received several loads of REDI-ROCK retaining wall block each day.
 - Crew continued to receive loads of No.57 stone for backfilling of the retaining wall.
 - Crew installed 241.50 sections of REDI-ROCK retaining wall block on the east wall.

- **PROPOSED PROGRESS OVER THE NEXT WEEK**
 - Delivery of additional No.57 stone for backfill of the REDI-ROCK retaining wall.
 - Sub-contractor will complete the backfilling and compaction of the west retaining wall.
 - Sub-contractor will complete the backfilling and compaction of the east retaining wall.
 - Sub-contractor is scheduled to start the installation of the chain-link fence.
 - Barrett plans on filling, compacting and grading the slopes at the end of the east and west REDI-ROCK retaining walls as per plans and specs.
 - The contractor will continue to work 7:00 AM to 3:30 PM. Monday thru Friday.

- **NEXT MEETING**
 - Progress Meeting No.2 is scheduled for Wednesday 15, 2019 at 2:00pm.
Location: Camden County Department of Public Works building.

Notice to Proceed Date: **October 14, 2019**
Contract Completion Date: **March 12, 2020**
Anticipated Completion Date: **March 12, 2020**

Prepared By: Dennis S. Brown, C.E.T.
Resident Engineer
Maser Consulting, P.A.

Dominic Vesper, Jr. Deputy County Administrator
John Wolick, Director of Camden County Department of Public Works
Kevin Becica, PE, Camden County Engineer
William England, P.E. Camden County Assistant Engineer
Paul K. Nolan, P.E., Senior Project Manager
Richard A. Brown, Project Manager
