



Berlin-Cross Keys Road and Kearsley Road Signalization Improvements Contract 1A Gloucester Township, Camden County, New Jersey Camden County

Maser Consulting Project No 19002364G2

Progress Report # 2 April 3, 2020



Figure 1: Crew installing Hot Mix Asphalt Base









Figure 2-3: Crew installing Asphalt curb









Figure 4-5: Crew cutting out roadway









Figure 6-7: Installing DGA and Hot Mix Asphalt Base





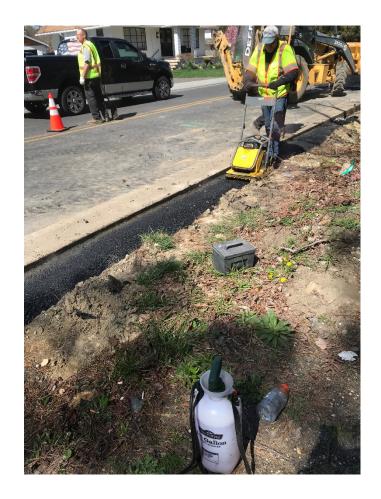


Figure 8: Crew installing Hot Mix Asphalt Base.





Think Paving, LLC mobilized on Tuesday, March 24 at 6:30am, and will continue to work for approximately 4 weeks.

• ITEMS COMPLETED THIS PAST WEEK

- o Excavating and grading SB side of Berlin Cross Keys Rd.
- o Installed 127 LF of Hot Asphalt curb
- o Installed a total of 691.9 sq/yds of Dense Graded Aggregate Base
- o Installed 135.17 TN of Hot Mix Asphalt Base.
- o A total of 160.43 TN as of April 3, 2020.

Prepared By: Franco DeGeorge Maser Consulting
