



IMPROVEMENTS TO WATSONTOWN-NEW FREEDOM ROAD (CR 691)

ERI Job # 30750 60

Boroughs of Berlin, Clementon, Lindenwold & Pine Hill

County of Camden, New Jersey

WEEKLY PROGRESS REPORT #22

July 6, 2020 to July 10, 2020



Figure: 1 – HMA milling in the southbound lane between Berlin-Clementon Road and Berlin-Cross Keys Road in the Borough of Pine Hill



Figure: 2 – Clearing of edge of paving after completion of milling in the northbound lane Berlin-Clementon Road and Berlin-Cross Keys Road in the Borough of Berlin

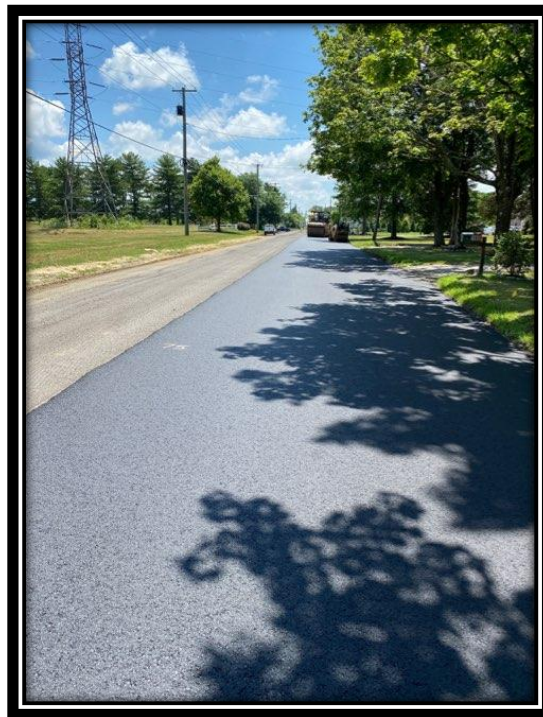


Figure: 3 – Installation of HMA 9.5M64 surface course along the southbound lane between Berlin-Clementon Road and Berlin-Cross Keys Road in the Borough of Pine Hill

Work Completed the Week of July 6, 2020:

South State's milling crew completed the HMA milling between Berlin-Clementon Road and Berlin-Cross Keys Road in the Berlin and Pine Hill section of the project. South State milled 35,233 square yards of the existing roadway. South State's paving crew then installed 2,263.69 tons of HMA 9.5M64 surface course in the southbound lane between Berlin-Clementon Road and Berlin-Cross Keys Road in the Borough of Pine Hill. Due to heavy rains on Friday, July 10th, top course paving of the northbound lane in the Borough of Berlin was postponed until Monday, July 13th. South State's punch list crew continued working on the preliminary punch list items in the Clementon section of the project.

#2: Police Uniform Law Enforcement Officer – 71 MH

#12: HMA Milling, 3" or Less – 35,233 SY

#15: HMA 9.5M64 Surface Course – 2,263.69 Tons

Anticipated Work for the Week of July 13, 2020:

South State's paving crew will complete the HMA 9.5M64 overlay of the northbound lane between Berlin-Cross Keys Road and Berlin-Clementon Road in the Berlin section of the project. The paving crew will then begin installation of HMA driveways in the Clementon section of the project. South State's punch list crew will continue working on the preliminary punch list items throughout the project.

Notice to Proceed Date: January 13, 2020

Anticipated Top Course Paving Start Date: July 13, 2020 (Berlin Borough)

Anticipated Completion Date: July 28, 2020

Prepared By:

A handwritten signature in blue ink, appearing to read 'C. J. Noll'.

C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
