

**Camden County Department of Public Works  
Division of Engineering  
Roadway and Drainage Improvements Evesham Road  
Runnemede Borough, Magnolia Borough and  
Gloucester Township, Camden County, New Jersey  
Progress Report No. 14  
September 12, 2022 to September 16, 2022**



*Figure 1: Manhole with frame*

**Work Completed Period of September 16, 2022**

- Removed 15" RCP and 18" DIP.
- 24" RCP installed to plan. Placed new inlet box/frame and manhole set and placed.
- Reconstructed existing inlet wall and replaced a casting.
- Asphalt trench restoration repairs.



Figure 2: Compacted DGA



Figure 3: Reconstructed inlet

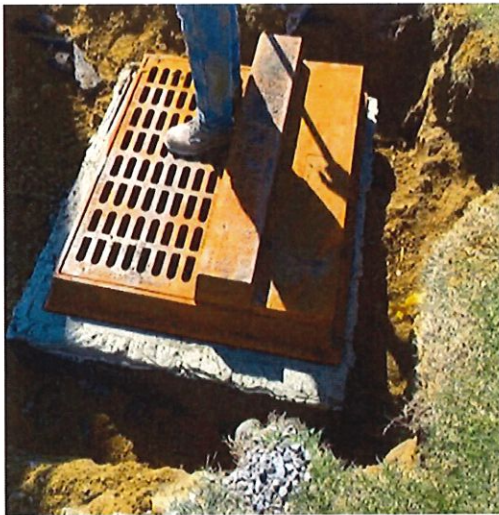


Figure 4: Inlet frame and grate



Figure 5: Reconstructed inlet

**Quantities Period of September 16, 2022**

- **Item #21:** Dense-Graded Aggregate Base Course, 6" Thick (162.64 SY)
- **Item #27:** Hot Mix Asphalt 19M64 Base Course (Trench Restoration) (90.51 TON)
- **Item #30:** 24" Reinforced Concrete Pipe (248 LF)
- **Item #36:** 15" Reinforced Concrete Pipe, Class V (14 LF)
- **Item #44:** Inlet, Type B (1 UNIT)
- **Item #49:** Manhole, 4" Diameter (1 UNIT)
- **Item #56:** Reconstructed Inlet, Type B, Using New Casting (3 UNIT)

**Summary of Work Completed Period of September 16, 2022**

The crew continued to run 24" RCP while removing existing 15" RCP and 18" DIP. Placed new inlet box and frame/grate, also reconstructed existing inlet walls, and placed new casting. Completed asphalt trench restoration repairs by placing DGA and base course and compacting.

**Anticipated Work for Period of September 19, 2022**


- Continue to install pipe, place manholes, and asphalt trench restoration repair as per plans.

**Notice to Proceed:** May 16, 2022

**Substantial Completion:** November 12, 2022

**Final Completion:** December 12, 2022

**Prepared By:**

  
Joseph R. Ragusa, P.E.  
Remington & Vernick Engineers
