Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Making It Better, Together.

Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

Berlin-Cross Keys Road Improvements Contract 3 Bid No. B9-22

Borough of Pine Hill and Townships of Gloucester and Winslow Camden County, New Jersey

CED Project No. 19002364G4

Progress Report #48 Monday, August 14, 2023 to Friday August 18, 2023



Figure: P&A Construction continues to install the hot mix aspahlt, using their brand new CAT AP 1055.

Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Making It Better, Together.

Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

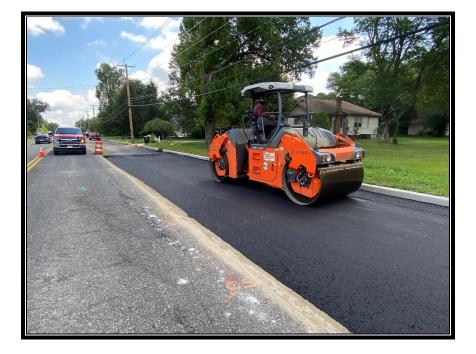


Figure 2: P&A Construction using a roller to ensure proper compaction.



Figure 3: P&A Construction removing an existing 24" R.C.P.

Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

• Work Completed this week:

- P&A Construction continued to build the widening part of the roadway.
- P&A Construction completed the installation of the dual vortex unit and pipe.
- P&A Construction continues to fine grade the D.G.A. and install the base course.

• Items completed this period:

- Item No.4 Traffic Safety Services Hours
- Item No.18 Tack Coat 20.50 Gallons
- o Item No.21 HMA 25.M64 Base Course, 4" Thick -1,721.69 Tons
- Item No.68 9"x18" Concrete Vertical Curb 130 L.F.

• Progress Next Two Weeks:

- P&A Construction will continue to fine grade the D.G.A. along the new widening area.
- P&A Construction will continue to install HMA 25.M64 Base Course in the widening area.
- P&A Construction will construct right-of-way transitions into several properties.

• Next Progress Meeting:

- The 18th Progress Meeting has been rescheduled for August 31, 2023 at 1:00pm on site. (This meeting may be rescheduled if necessary or become a Microsoft Teams Meeting)
 - Bid Opening Date: June 2, 2022
 - Notice to Proceed: August 23, 2021
 - Start Date: August 23, 2021
 - Substantial Completion Date: July 24, 2023
 - Stop Work: N/A
 - Amended NTP: N/A
 - Final Completion Date: August 23, 2023
 - Initial Award: \$6,946,586.14

Prepared by: Dennis S. Brown, C.E.T. Resident Engineer Colliers Engineering & Design

James Winckowski, PE, County Engineer William England, PE, Assistant County Engineer
