



**CHURCH ROAD (CR 616) ROADWAY IMPROVEMENTS**

**Federal Project No. STBGP-PHILA-0613(301)**

**NJDOT Job No. 5809322**


**ERI Job #:30750 71**

**Township of Cherry Hill**

**County of Camden, New Jersey**

**WEEKLY PROGRESS REPORT #2**

**April 3, 2023 to April 7, 2023**

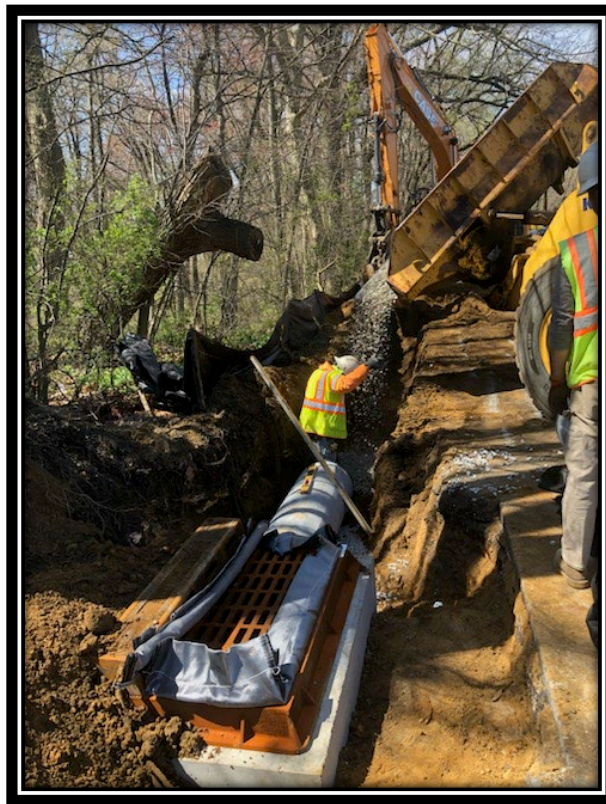

*Figure: 1 – Installation of 15” RCP along the eastbound lane between Kings Croft Drive and the County Border*



*Figure: 2 – Installation of 12” DIP crossing between Kings Croft Drive and the County Border*



*Figure: 3 – Installation of twin 12” DIP along the eastbound lane between Kings Croft Drive and the County Border*

**Work Completed the Week of April 3, 2023:**

Black Rock's pipe crew continued installation of drainage improvements along the eastbound lane between King's Croft Drive and Crofton Commons. The pipe crew installed 76 linear feet of 12" DIP, 157 linear feet of 15" RCP and 1 B inlet.

**#5: Police-Uniform Law Enforcement Officer – 67 MH**

**#21: 12" Ductile Iron Pipe – 76 LF**

**#25: 15" Reinforced Concrete Pipe, Class IV – 157 LF**

**#28: Inlet, Type 'B', Complete – 1 Unit**

**Anticipated Work for the Week of April 10, 2023:**

South State's pipe crew will continue installation of the proposed storm sewer improvements along the eastbound lane between King's Highway and Crofton Commons.

**Bid Opening Date: March 31, 2023**

**Amended Notice to Proceed Date: March 27, 2023**

**Start Date: March 27, 2023**

**Anticipated Completion Date: December 1, 2023**

**Contract Completion Date: December 31, 2023**

**Contract Completion Percentage: 6.48%**

Prepared By:



C. Jeremy Noll, PE, CME, CPWM  
Resident Engineer  
Environmental Resolutions, Inc.
