

LITTLE GLOUCESTER ROAD (CR 759) ROADWAY IMPROVEMENTS

ERI Job #:30750 78

Township of Gloucester

County of Camden, New Jersey

BI-WEEKLY PROGRESS REPORT #1

November 13, 2023 to November 24, 2023

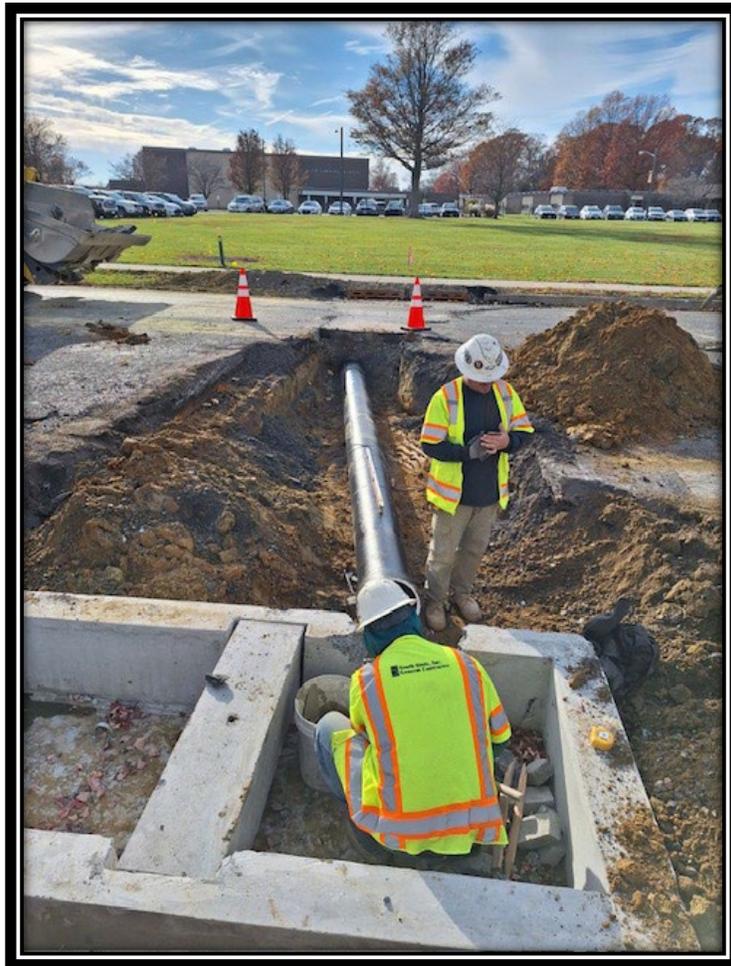


Figure: 1 – Installation of Type Double B Inlet and 12” DIP between Chews Landing Road and Seabury Drive



Figure: 2 – Installation of 18” RCP along the southbound lane between Chews Landing Road and Seabury Drive

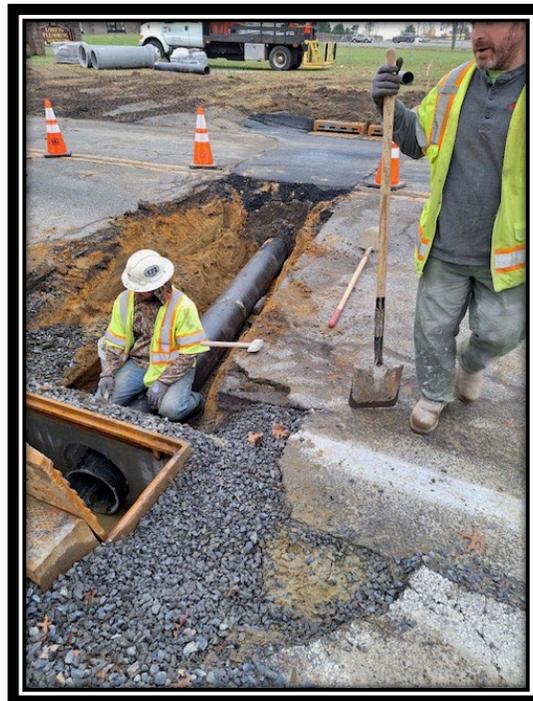


Figure: 3 – Installation of Type Double B Inlet and 12” DIP between Chews Landing Road and Seabury Drive

Work Completed the Weeks of November 13, 2023 and November 20, 2023:

The contractor, South State, Inc., mobilized to the site on Monday, November 13, 2023. South State's pipe crew began installation of drainage improvements along both the southbound and northbound lanes between Chews Landing Road and Seabury Drive. The pipe crew installed 130.5 linear feet of 12" DIP, 376 linear feet of 18" RCP, 24 linear feet of 24" RCP and 4 Double B inlets. They also repaired the joint at an existing 12" RCP.

- #5: VMS Board – 2 Units**
- #6: Traffic Safety Services – 72 MH**
- #19: 12" DIP – 103.5 LF**
- #20: 18" RCP – 376 LF**
- #21: 24" RCP – 24 LF**
- #22: Joint Repair, 12" RCP – 1 Unit**
- #26: Inlet, Type Double 'B' – 4 Units**

Anticipated Work for the Weeks of November 27, 2023 and December 4, 2023:

South State's pipe crew will continue installation of the proposed storm sewer improvements along the eastbound lane between Chews Landing Road and Blackwood-Clementon Road.

- Bid Opening Date: July 12, 2023**
- Notice to Proceed Date: November 13, 2023**
- Start Date: November 13, 2023**
- Anticipated Completion Date: April 10, 2024**
- Contract Completion Date: May 10, 2024**
- Contract Completion Percentage: 20.49%**
- Initial Project Cost: \$1,559,525.00**

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
