

LITTLE GLOUCESTER ROAD (CR 759) ROADWAY IMPROVEMENTS

ERI Job #:30750 78

Township of Gloucester

County of Camden, New Jersey

BI-WEEKLY PROGRESS REPORT #2

November 27, 2023 to December 8, 2023



Figure: 1 – Installation of Type Double B Inlet along the southbound lane between Golf View Drive and Hider Lane

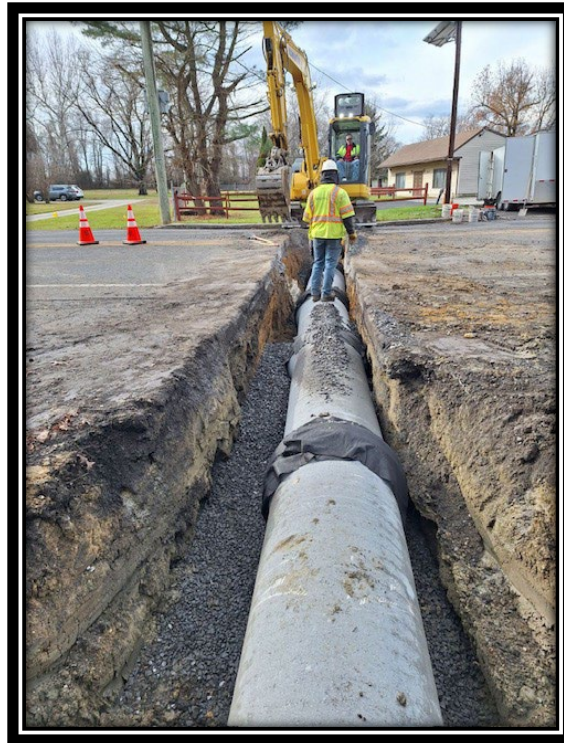


Figure: 2 – Installation of 24” RCP crossing between Tall Oaks Drive and Mt. Pleasant Road



Figure: 3 – Installation of 24” Flared End Section between Tall Oaks Drive and Mt. Pleasant Road

Work Completed the Weeks of November 27, 2023 and December 8, 2023:

South State's pipe crew completed the installation of drainage improvements along both the southbound and northbound lanes for the entire project except for inlet head and grate replacements. The pipe crew installed 23 linear feet of 18" RCP, 69 linear feet of 24" RCP, 6 Double B inlets, 1 flared end section and reconstructed 1 existing inlet. They also repaired 3 joints along the existing 15" RCP.

#6: Traffic Safety Services – 132 MH

#20: 18" RCP – 23 LF

#21: 24" RCP – 69 LF

#23: Joint Repair, 15" RCP – 3 Units

#26: Inlet, Type Double 'B' – 6 Units

#27: Flared End Section – 1 Unit

#S1: Reconstruct Inlet – 1 Unit

Anticipated Work for the Weeks of December 11, 2023 and December 18, 2023:

South State will shut down for the winter and resume the project in early spring of 2024. At that time, a revised notice to proceed will be issued.

Bid Opening Date: July 12, 2023

Notice to Proceed Date: November 13, 2023

Revised Notice to Proceed Date: Early Spring 2024 (exact date TBD)

Start Date: November 13, 2023

Anticipated Completion Date: May 31, 2024

Original Contract Completion Date: May 10, 2024

Revised Contract Completion Date: Early Summer 2024 (exact date TBD)

Contract Completion Percentage: 28.99%

Initial Project Cost: \$1,559,525.00

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
