

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

**Park Avenue (CR 621) Roadway Improvements
From Cove Road (CR 616) to Union Avenue (CR 651)**

*Township of Pennsauken, Borough of Merchantville
Camden County, New Jersey
Bid No. B5-21*

CED Project No. 21000047G1

Progress Report # 23
Monday, June 20, 2022 to Friday, June 24, 2022

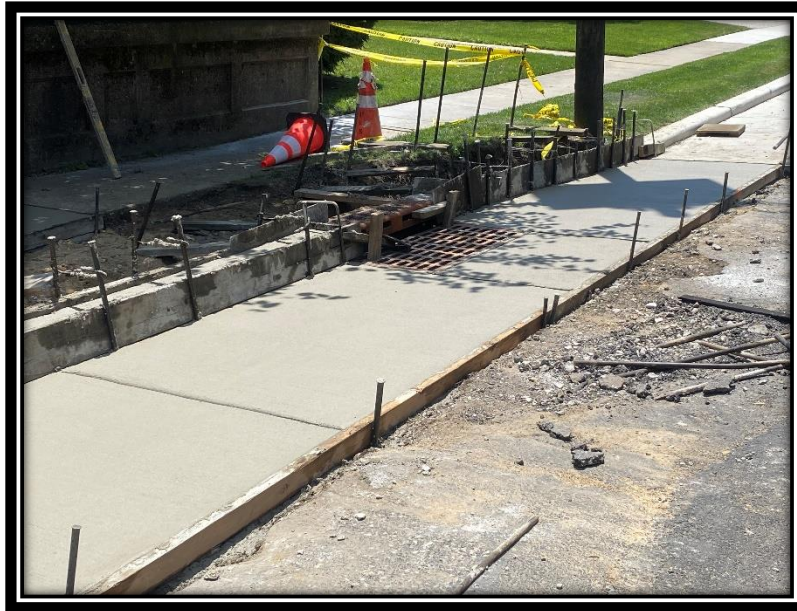


Figure 1: Completed gutter line.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com



Figure 2: Continue Sidewalk on Park Avenue.



Figure 3: Completed form work for concrete sidewalk and gutter line.

- **Work Completed this week:**

Contractor resumed concrete work at the north end of the project including sidewalk, curb, and gutter line.

Items completed this period:

#12	HMA 9.5M64 Surface Course	2 tons
#26:	Concrete Sidewalk, 4" Thick	38 SY
#27:	Concrete Driveway, 6" Thick	6 SY
#30:	Monolithic Curb and Gutter, 4' Wide	45 LF

- **Progress Next Two Weeks:**

- Completion of drainage pending relocation of gas main on Cooper Avenue.

- **Next Meeting:**

- The next progress meeting is not scheduled.

- Bid Opening Date: May 4, 2021
- Notice to Proceed: August 2, 2021
- Start Date: August 3, 2021
- Substantial Completion Date: January 29, 2022
- Stop Work: November 23, 2021
- Amended NTP: April 11, 2022
- Final Completion Date: July 17, 2022
- Initial Award: \$1,808,833.93

Prepared by: Kaitlin Flanagan,
Construction Observer
Colliers Engineering & Design
