

Department of Public Works

Susan Shin Angulo
Freeholder Liaison

John Wolick
Director



Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com



Clementon-Berlin Road (CR 534) Bridge over North Branch of Timber Creek Structure No. 048E006

Borough of Clementon
County of Camden, NJ
Weekly Progress Report #22
March 4 to March 8, 2019




Zone painted highway markings for the next Stage. Traffic was moved into Stage 3 on Monday the 4th



SJ Gas sub was in to shut down gas main going over the existing Bridge



Demo began at the retaining wall once JMT obtained permit from NJDEP

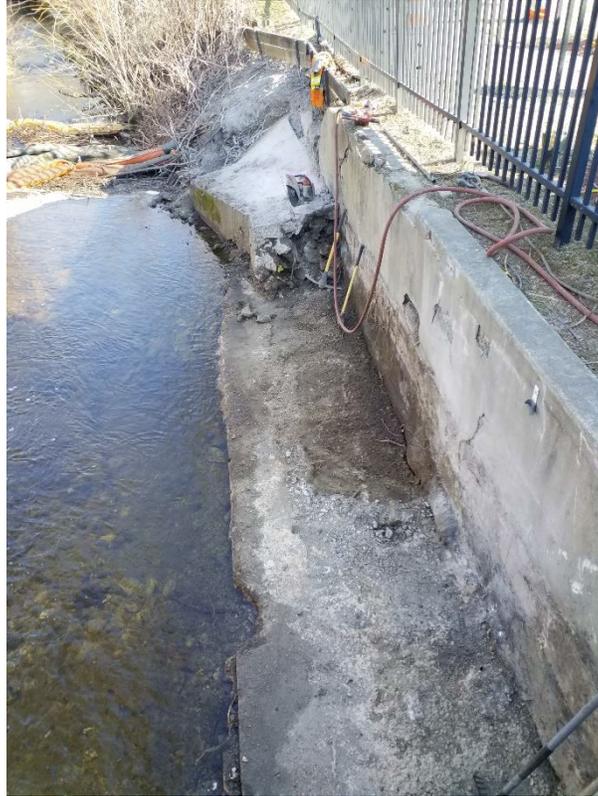

All existing material was removed to allow new wall to be built



Contractor installed the rebar anchors as per the plan developed by JMT

Partial NTP : August 15, 2018
NTP : September 20, 2018

Contractor Duration: 512 days
Completion date February 14, 2020

33.2% of time used to date

58.4% paid to date

The Notice to Proceed was given on September 20, 2018. Contractor has the duration of 512 days making the completion date on February 14, 2020.

Contractor moved traffic into Stage 3 on Monday March 4th. SJ Gas sub-contractor was on site March 5th to shut down the gas main crossing the existing structure. This will allow the contractor to demo the existing structure and without an active gas main. The main will be replaced later in this stage. JMT was able to procure an emergency permit from NJDEP and strengthen the existing retaining wall next to the park on the NE area of the project. Demolition started and installation of rebar anchors were installed as per the plan provided by JMT.

Next week the contractor will continue the retaining wall and may start clearing of the waterway between the new structure and the Dam on E. Atlantic. It should be noted that both the retaining wall work and clearing the waterway are extra activities to the project.

Prepared by: Tony Guerrieri, AECOM Project Manager
