

Department of Public Works

Susan Shin Angulo
Freholder Liaison

John Wolick
Director



Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com



**Clementon-Berlin Road (CR 534) Bridge over
North Branch of Timber Creek Structure No. 048E006**

Borough of Clementon
County of Camden, NJ
Weekly Progress Report #3
September 3 to September 7, 2018



Forming curb at the Temporary Driveway



Sidewalk to be poured for the Temporary Driveway at Clementon Lake Plaza



Pouring Sidewalk for the Temporary Driveway



Temporary Driveway at Clementon Lake Plaza after it was paved



Boxed-out area where roadway will be widened and temporary sidewalk to be constructed


Partial NTP : August 15, 2018

Contractor Duration: 512 days

A Partial Notice to Proceed was given to allow the contractor to start work on the Temporary Driveway for the Plaza, Set the Pedestrian Bridge, and install water main wet taps to permit for water bypass.

Utility Companies continue to relocate the aerial lines onto the temporary poles that were set. ACE has completed their work. Verizon just needs to remove the existing poles once Comcast and Sunesys are no longer on the poles. Currently Comcast is installing their new line and just needs to splice. Then Sunesys can just transfer the existing line onto the new temporary poles since they have enough slack in the wire.

Midlantic finished the Temporary Driveway for Clementon Lake Plaza. They continue to work on the area between the temporary driveway and the existing driveway for the Plaza. This area widens the roadway for a future stage in the project, but more importantly constructs a temporary sidewalk on the south side. Currently the plans close this sidewalk and cross the pedestrian to the north existing sidewalk. The Police Chief has expressed his dislike in this plan, but understands that the County has approved the plans. The plans allow the pedestrian to cross at Park Blvd and Gibbsboro Road. The Chief requested we move the Park Blvd crossing to White Horse since it is an existing Traffic Signal and there is a Crossing Guard at this location. Clementon is a walking school district so all the kids need to walk to school. The hope is that the week of September 17th this temporary sidewalk will be completed up to the existing driveway for the Plaza. Midlantic will continue to construct the Temporary Pedestrian Bridge which then will be the new access through the project. See below for highlighted sidewalk.

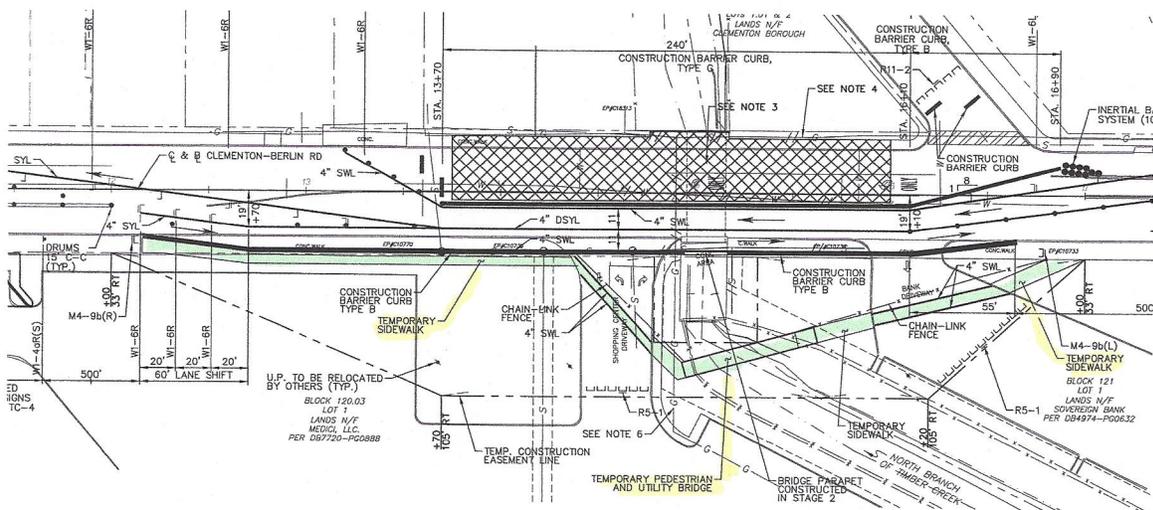

Prepared by: Tony Guerrieri, AECOM Project Manager
