

Department of Public Works

Susan Shin Angulo
Freeholder Liaison

John Wolick
Director




Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com



Clementon-Berlin Road (CR 534) Bridge over North Branch of Timber Creek Structure No. 048E006

Borough of Clementon
County of Camden, NJ
Weekly Progress Report #37
July 01 to July 05, 2019

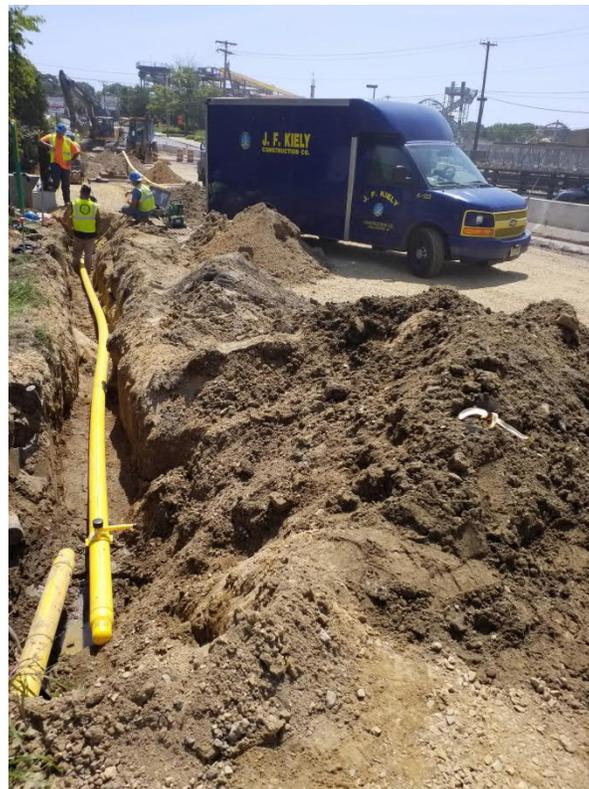

Gas lines reconnected



Grading DGA for sidewalk and curb



Pouring Vertical curb



Pouring full depth depressed vertical curb for driveway



Curb at Garfield and Clementon – Berlin road



Curb at Senior center

Partial NTP : August 15, 2018
NTP : September 20, 2018

Contractor Duration: 512 days
Completion date February 14, 2020

56.2 % of time used to date

79.1 % paid to date

The Notice to Proceed was given on September 20, 2018. Contractor has the duration of 512 day making the completion date on February 14, 2020.

The contractor for South Jersey Gas (J.F. Kiely) reconnected the gas lines.

MidLantic graded the DGA for the sidewalk and vertical curb.

Vertical curb installed from Garfield avenue to in front of Senior center.

Prepared by: Tony Guerrieri, Jim Carrigan, AECOM
