



**IMPROVEMENTS TO WATSONTOWN-NEW FREEDOM ROAD (CR 691)**

**ERI Job # 30750 60**

**Boroughs of Berlin, Clementon, Lindenwold & Pine Hill**


**County of Camden, New Jersey**

**WEEKLY PROGRESS REPORT #15**

**May 18, 2020 to May 22, 2020**



*Figure: 1 – Installation of ADA ramp at the southwest corner of the intersection Watsonstown-New Freedom Road (CR 691) and Berlin-Clementon Road in the Borough of Clementon*

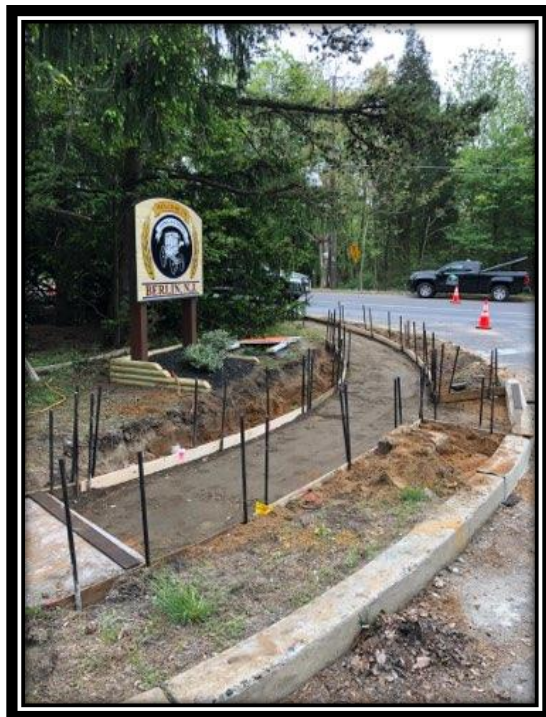

*Figure: 2 – Installation of ADA ramp at the northeast corner of the intersection Watsontown-New Freedom Road (CR 691) and Berlin-Clementon Road in the Borough of Clementon*



*Figure: 3 – Installation of concrete curb adjacent to the newly reconstructed type 'B' inlet in the southbound lane between Berlin-Clementon Road and Berlin-Cross Keys Road*

**Work Completed the Week of May 18, 2020:**

South State's concrete crew continued concrete improvements in the Pine Hill section of the project. The concrete crew installed 258 linear feet of concrete curb, 76.8 square yards of concrete sidewalk and 7 square yards of detectable warning surface. The concrete crew installed 7 ADA ramps at the intersection of Watsontown-New Freedom Road and Clementon-Berlin Road.

**#2: Police Uniform Law Enforcement Officer – 80 MH**

**#33: Concrete Sidewalk, 4" Thick – 76.8 SY**

**#36: Detectable Warning Surface – 7 SY**

**#37: 9" x 18" Concrete Vertical Curb – 258 LF**

**Anticipated Work for the Week of May 25, 2020:**

South State's concrete crew will continue concrete improvements in the Berlin & Pine Hill portion of the project between Berlin-Clementon Road and Berlin Cross Keys Road. South State will also replace the remaining non compliant inlet heads in the Berlin section of the project.

**Notice to Proceed Date: January 13, 2020**

**Anticipated Completion Date: July 28, 2020**

Prepared By:

A handwritten signature in blue ink, appearing to read 'C. J. Noll'.

C. Jeremy Noll, PE, CME, CPWM  
Resident Engineer  
Environmental Resolutions, Inc.
