

Bid No. B8-21: Roadway Improvements Along Evesham Road (CR 544)


From US Route 30 (MP 5.40) to Burnt Mill Road (MP 6.50)

Borough of Magnolia, Lawnside, and Somerdale

Townships of Cherry Hill and Voorhees

Progress Report #2

Week Ending November 19, 2021

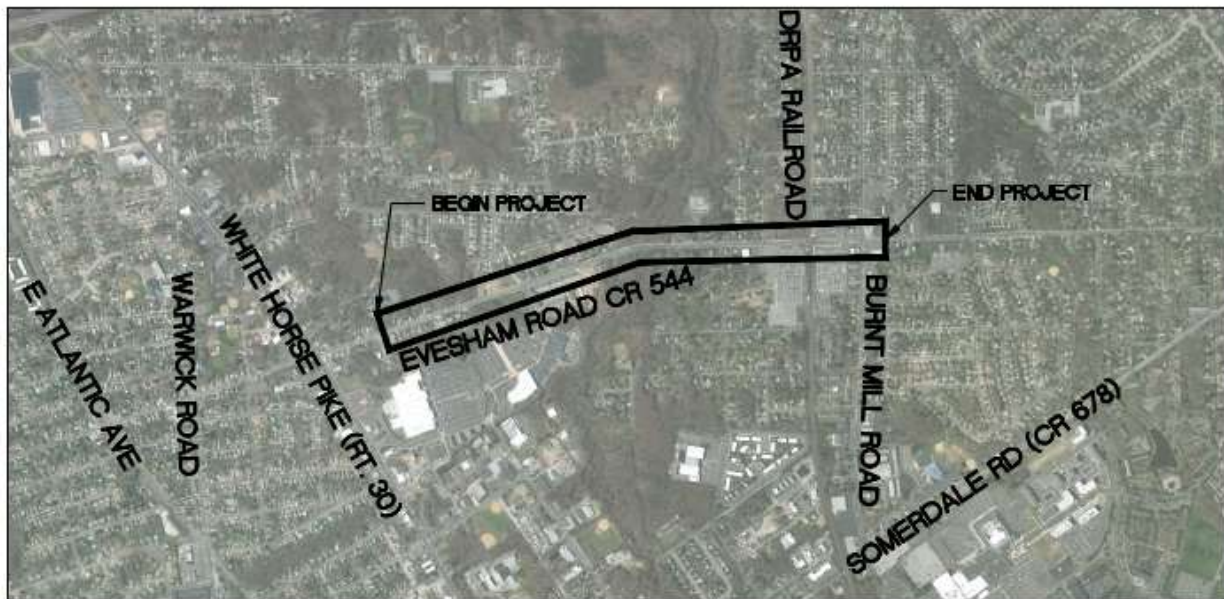



Work Completed this Week:

- Contractor was not on site this week.

Work Projected for Next Week:

- Contractor continuing preparation for curb/sidewalk and drainage work on Evesham Road.

Project Schedule:

- **Bid Opening Date:** Tuesday, June 29th, 2021
- **Notice to Proceed:** Wednesday, November 3rd, 2021
- **Start Date:** Wednesday, November 10th, 2021
- **Substantial Completion Date:** Saturday, April 2nd, 2022
- **Stop Work:** N/A
- **Amended NTP:** N/A
- **Final Completion Date:** Friday, April 22nd, 2022
- **Initial Award:** \$2,403,571.30

Prepared by:

Haris Ansari
Resident Engineer
Naik Consulting Group
