


# Construction Management and Inspection Services



**CHURCH ROAD (CR 616) ROADWAY IMPROVEMENTS, B3-22**  
**Federal Project No. STBGP-PHILA-0613(301)**  
**NJDOT Job No. 5809322**  
**ERI Job #:30750 71**  
**Township of Cherry Hill**  
**County of Camden, New Jersey**


**BI-WEEKLY PROGRESS REPORT #22**  
**September 18, 2023 to September 29, 2023**

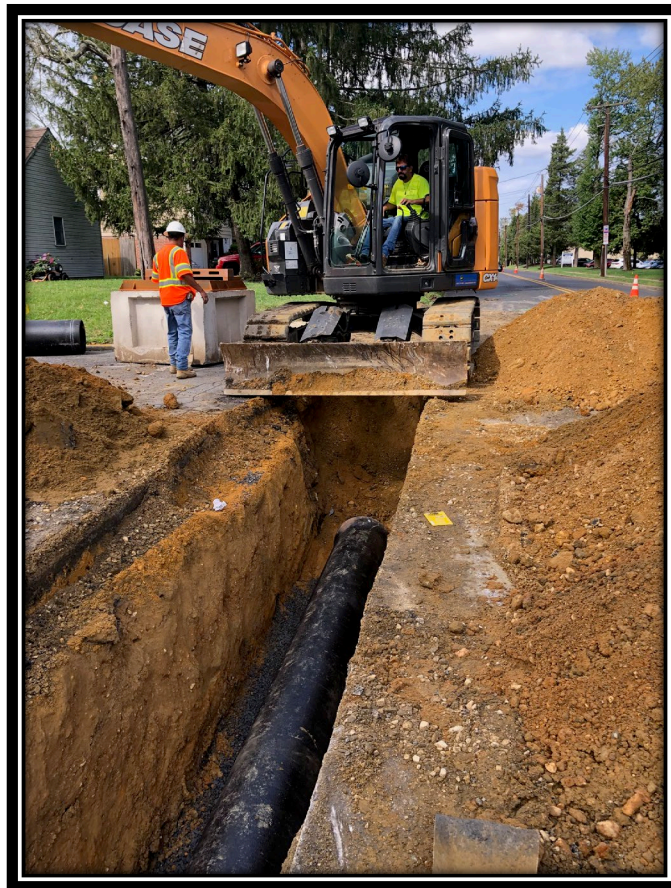

*Figure: 1 – Installation of 18” DIP along the eastbound lane at the intersection with West Lake Drive*



*Figure: 2 – Installation of concrete curb, sidewalk and driveway apron along the eastbound lane between Columbia Boulevard and Lake Drive East*

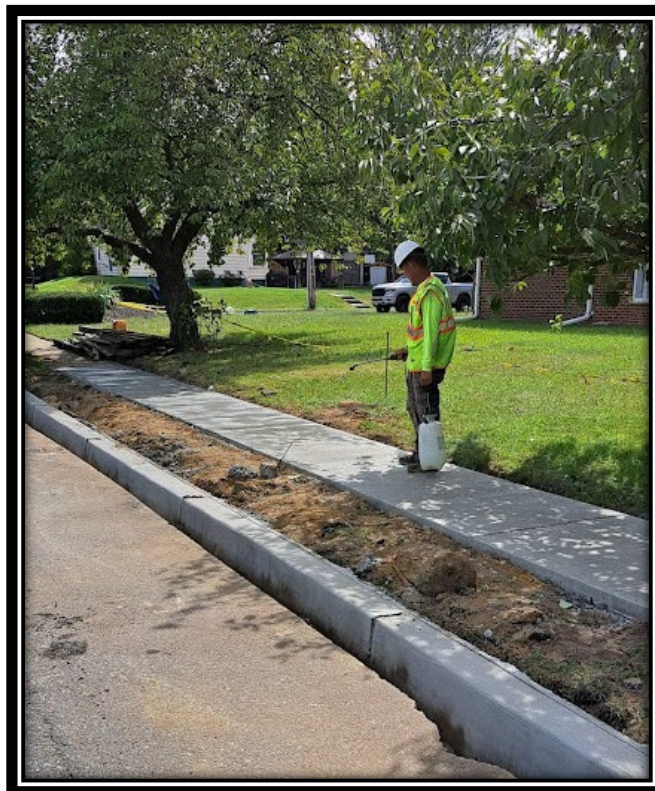

*Figure: 3 – Spraying of curing compound on newly installed concrete curb and sidewalk along the eastbound lane between Wilson Road and Columbia Boulevard*

**Work Completed the Weeks of September 18, 2023 & September 25, 2023:**

Black Rock's concrete subcontractor, Discover Construction, continued concrete improvements along the eastbound lane between Wilson Road and Lake Drive West. Discover installed 342.56 square yards of concrete sidewalk, 1,770 linear feet of concrete vertical curb, 104.04 square yards of 6" thick, reinforced concrete driveway apron and 5.28 square yards of detectable warning surface. Black Rock's pipe crew continued drainage improvements between Lake Drive East and Oak Avenue. Black Rock installed 1 type B inlet, 1 modified type B inlet, 77 linear feet of 18" DIP, 154 linear feet of 18" RCP and 2 inlet filters.

- #5: Police-Uniform Law Enforcement Officer – 126 MH**
- #24: 18" DIP – 77 LF**
- #26: 18" RCP – 154 LF**
- #28: Type 'B' Inlet – 1 Unit**
- #40: Concrete Sidewalk, 4" Thick – 244.82 SY**
- #42: Concrete Driveway, Reinforced, 6" Thick – 104.04 SY**
- #43: Detectable Warning Surface – 5.28 SY**
- #44: 9" x 16" Concrete Vertical Curb – 1,770 LF**
- #71: Inlet Filter, Type 2, 2'x4' – 2 Units**
- #CH1: Concrete Sidewalk, 4" Thick (Cherry Hill) – 97.74 SY**
- #S2: Type 'B' Inlet, Modified – 1 Unit**

**Anticipated Work for the Weeks of October 2, 2023 & October 9, 2023:**

Discover Construction will continue concrete improvements along the eastbound and westbound lanes between Cleveland Avenue and Lake Drive West. They will also install the additional proposed sidewalk along the eastbound lane between the Cherry Valley Swim Club and King's Highway. Black Rock will continue drainage improvements between Lake Drive East and Oak Avenue.

**Bid Opening Date: March 31, 2022**

**Amended Notice to Proceed Date: March 27, 2023**

**Start Date: March 27, 2023**

**Anticipated Completion Date: December 1, 2023**

**Contract Completion Date: December 31, 2023**

**Contract Completion Percentage: 41.20%**

**Initial Project Cost: \$4,200,000.00**

Prepared By:



C. Jeremy Noll, PE, CME, CPWM  
Resident Engineer  
Environmental Resolutions, Inc.
