



CHURCH ROAD (CR 616) ROADWAY IMPROVEMENTS, B3-22
Federal Project No. STBGP-PHILA-0613(301)
NJDOT Job No. 5809322
ERI Job #:30750 71
Township of Cherry Hill
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #14
June 26, 2023 to June 30, 2023

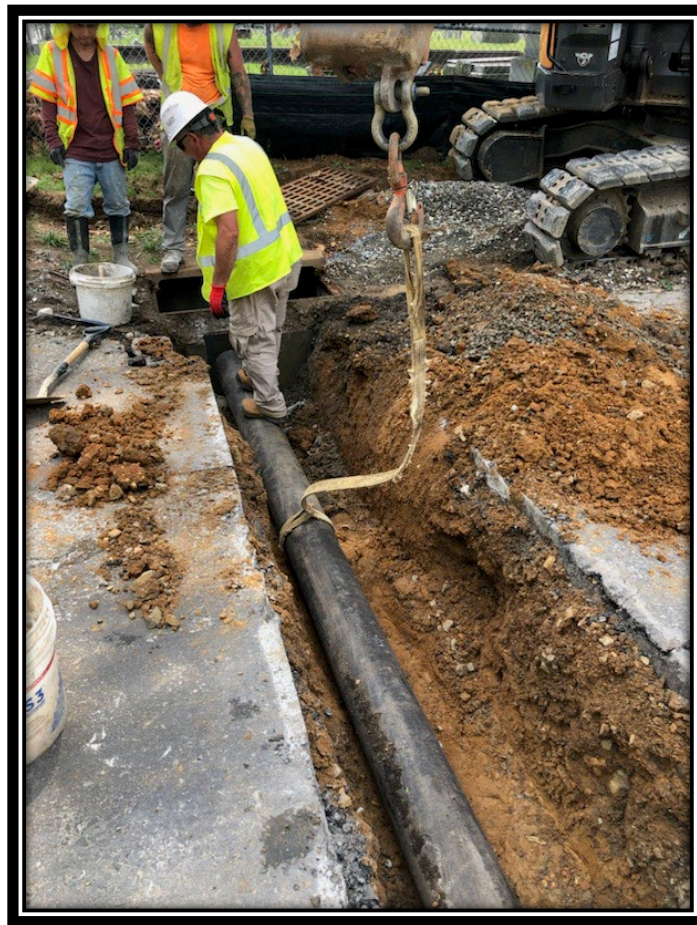


Figure: 1 – Installation of 12” DIP storm sewer at the intersection with Friendship Lane



Figure: 2 – Installation of 12” DIP storm sewer at the intersection with Friendship Lane



Figure: 3 – HMA trench restoration over newly installed 12” DIP storm sewer at the intersection with Friendship Lane

Work Completed the Week of June 26, 2023:

Black Rock's pipe crew completed the storm sewer crossings between Friendship Lane and Kings Highway. The pipe crew installed 30 linear feet of 12" DIP.

#5: Police-Uniform Law Enforcement Officer – 17 MH

#21: 12" Ductile Iron Pipe – 30 LF

Anticipated Work for the Week of June 26, 2023:

Black Rock's pipe crew will leave the project for approximately 3 weeks while their concrete subcontractor, Discover Construction, mobilizes to begin concrete improvements. Discover will start concrete improvements on July 5th and work along the westbound lane between the County border and King's Croft Drive.

Bid Opening Date: March 31, 2022

Amended Notice to Proceed Date: March 27, 2023

Start Date: March 27, 2023

Anticipated Completion Date: December 1, 2023

Contract Completion Date: December 31, 2023

Contract Completion Percentage: 20.30%

Initial Project Cost: \$4,200,000.00

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
