



CHURCH ROAD (CR 616) ROADWAY IMPROVEMENTS, B3-22
Federal Project No. STBGP-PHILA-0613(301)
NJDOT Job No. 5809322
ERI Job #:30750 71
Township of Cherry Hill
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #6
May 1, 2023 to May 5, 2023

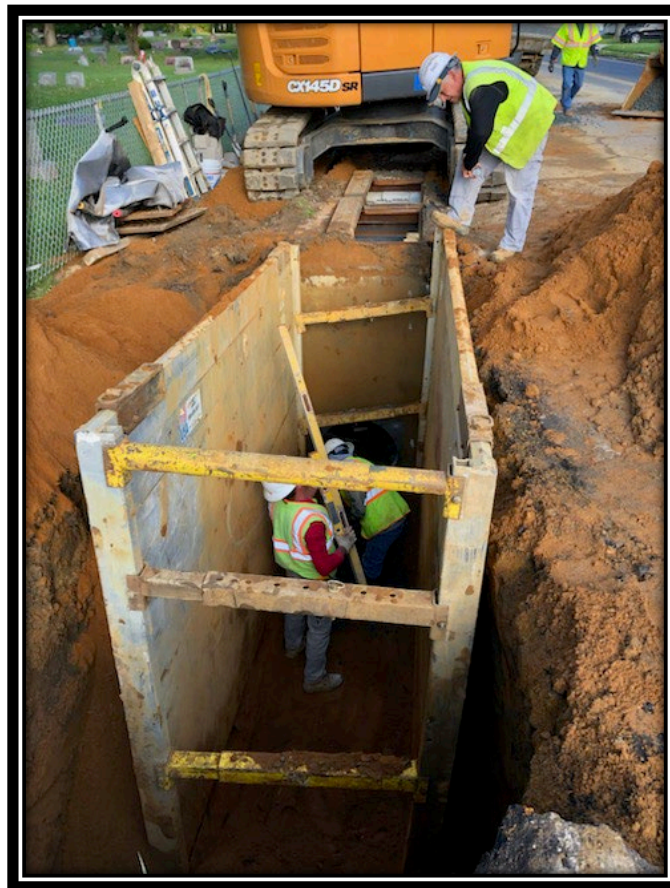


Figure: 1 – Connection of 18” RCP into a newly installed Double B Inlet along the eastbound lane between Millstream Drive and Friendship Lane



Figure: 2 – Installation of 18” RCP storm sewer along the eastbound lane between Millstream Drive and Friendship Lane



Figure: 3 – Compaction of newly installed 18” RCP trench along the eastbound lane between Millstream Drive and Friendship Lane

Work Completed the Week of May 1, 2023:

Black Rock's pipe crew continued installation of drainage improvements along the eastbound and westbound lanes between Friendship Lane and Millstream Drive. The pipe crew installed 336 linear feet of 18" RCP.

#5: Police-Uniform Law Enforcement Officer – 74 MH

#26: 18" Reinforced Concrete Pipe, Class IV – 336 LF

Anticipated Work for the Week of May 8, 2023:

Black Rock's pipe crew will continue the installation of the proposed storm sewer improvements between Friendship Lane and Cleveland Avenue along both the eastbound and westbound lanes.

Bid Opening Date: March 31, 2022

Amended Notice to Proceed Date: March 27, 2023

Start Date: March 27, 2023

Anticipated Completion Date: December 1, 2023

Contract Completion Date: December 31, 2023

Contract Completion Percentage: 12.40%

Initial Project Cost: \$4,200,000.00

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
