

Construction Management and Inspection Services



**BURNT MILL ROAD (CR 670) ROADWAY IMPROVEMENTS**


**ERI Job #:30750 73**

**Township of Voorhees**

**County of Camden, New Jersey**

**WEEKLY PROGRESS REPORT #4**

**March 20, 2023 to March 24, 2023**

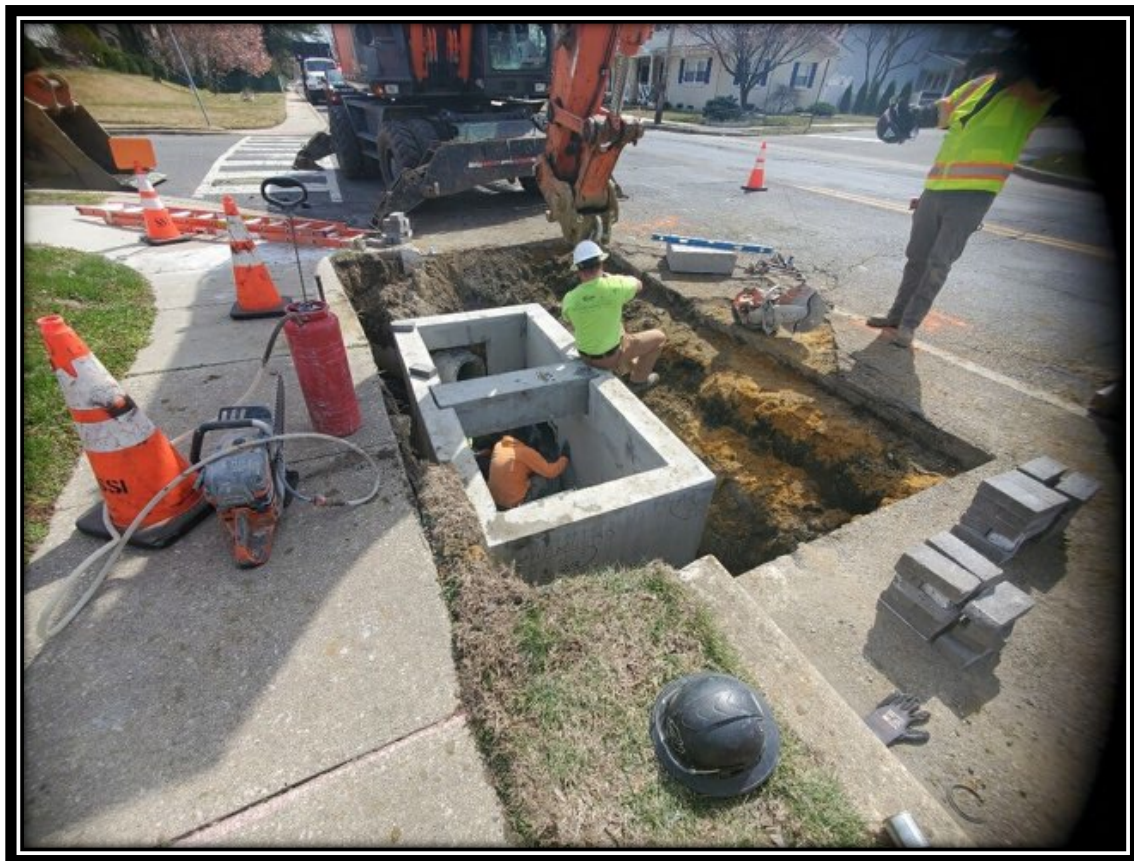

*Figure: 1 – Installation of Type Double B Inlet along the northbound lane at the intersection with Maple Avenue*



*Figure: 2 – Removal of existing Type B Inlet along the northbound lane at the intersection with Poplar Avenue*



*Figure: 3 – HMA restoration in front of newly installed Type B Inlet and temporary HMA sidewalk along the northbound lane between Britton Place and Cedar Avenue*

**Work Completed the Week of March 20, 2023:**

South State's pipe crew continued installation of drainage improvements along the northbound lane between Britton Place and Poplar Avenue. The pipe crew installed 3 Double B inlets. All trench restoration and disturbed sidewalk was restored with hot mix asphalt.

**#2: Traffic Safety Services – 27 MH**

**#19: Inlet, Type Double 'B' – 3 Units**

**Anticipated Work for the Week of March 27, 2023:**

South State's pipe crew will continue installation of the proposed storm sewer improvements along both the southbound and northbound lanes between Somerdale Road and Linden Avenue.

**Bid Opening Date: June 21, 2022**

**Notice to Proceed Date: February 2, 2023**

**Start Date: February 27, 2023**

**Anticipated Completion Date: June 30, 2023**

**Contract Completion Date: August 1, 2023**

**Contract Completion Percentage: 7.40%**

Prepared By:



C. Jeremy Noll, PE, CME, CPWM  
Resident Engineer  
Environmental Resolutions, Inc.
