

Department of Public Works

Susan Shin-Angulo  
Freeholder Liaison

John Wolick  
Director



Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988  
[highway@camdencounty.com](mailto:highway@camdencounty.com)

**East Atlantic Avenue (C.R. 729)  
over Nicholson Road (C.R. 635)  
Bridge Replacement Project**

*Borough of Audubon  
County of Camden, New Jersey  
Weekly Progress Report  
Monday 12/11/2017 thru Friday 12/15/2017*



**Figure 1**  
*Excavating test pit to locate existing water main*

Department of Public Works

Susan Shin-Angulo  
Freeholder Liaison

John Wolick  
Director




Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988

[highway@camdencounty.com](mailto:highway@camdencounty.com)



**Figure 2**

*R.E. Pierson sawcutting Nicholson Road (South Side)*

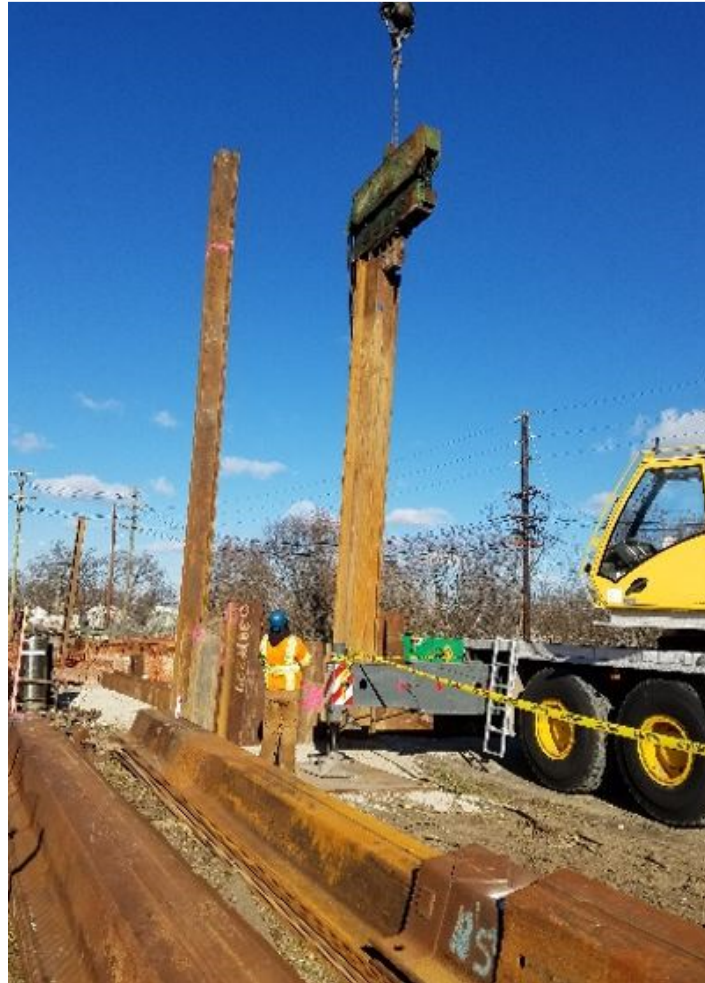

**Figure 3**

*Installation of Temporary Sheet Piling (South Side)*



**The following Construction Activities took place during the period stated above.**

### **Water Main / NJ American Water**

On Monday, December 11, 2017 Contractor excavated and hand excavated test pit along North side of Nicholson Road in sidewalk area to locate existing water main. Note: No water main was found in way of sheeting drive area. While driving a temporary sheet pile at NE corner, R.E. Pierson hit a water main at approximately 11 am. NJ American Water Company was called, and a representative arrived on site at approx. 11:30 am. Audubon PD was also on site at 11:30 am. NJ American Water Company shut off water at approx. 12 pm. R.E. Pierson took road plates off Nicholson Road, cleaned up roadway and backfilled test pit. NJ American Water and Pioneer Pipe replaced section of water main after work hours. R.E. Pierson drove temporary sheeting to finish grade at Conrail North side.

### **Temporary Sheeting**

Contractor installed sheeting on south Conrail side and the south side of bridge.

### **Traffic Safety**

On Wednesday, December 13, 2017, a Camden County representative installed a Variable Message Board to Taylor Avenue and Route 30 EB. Message on VMS reads "Nicholson Road Detour / Use Kings Highway"

### **Anticipated Work for the 12/18/17 thru 12/22/17**

The installation of sheeting is on hold until the watermain is relocated. The test pit for the watermain is scheduled for Tuesday, December 19, 2017.

For the north abutment, work includes the excavation around sheeting for the installation of tiebacks and the disposal of regulated material. For the south abutment, work includes the installation of sheeting.

**Notice to Proceed:** 09/28/17

**Anticipated Completion Date:** 11/20/18

**Prepared By:** Alfred Brenner  
Resident Engineer
