



**Mill and Overlay of Westfield Avenue (CR 610) from Tinsman Avenue (MP 1.57) TO NJ Route 130 (MP 2.92)  
Pennsauken Township, Camden County, New Jersey**

**Notice to Proceed issued: August 30, 2019**  
**Project Completion: May 10, 2020**  
**Project Substantial Completion: April 10, 2020.**  
**Project start: September 4, 2019.**

**Weekly Progress Report**  
**10-21-2019 through 10-25-2019**

**Following Construction Activities took place during above period:**

**Concrete Curb and Sidewalk:**

- a. Contractor was not present at site therefore construction activities were not performed.

**Drainage:**

- a. Existing Type B inlet along Holinshed Avenue West was Reconstructed using new casting, And Curb piece, Type N ECO was installed.
- b. Curb piece, Type N ECO were installed for three inlets along Westfield Avenue, LT between Hillcrest Avenue and Holinshed Avenue.
- c. 15" Reinforced Concrete Pipe, Class IV was installed across Horner Avenue, LT.
- d. 15" Reinforced Concrete Pipe was installed from inlet along Westfield Avenue to East Inlet along Horner Avenue, LT.
- e. 24" Reinforced Concrete Pipe, Class IV was installed across Westfield Avenue at Hillcrest Avenue.
- f. 18" Reinforced Concrete Pipe was installed along Westfield Avenue, LT Between Hillcrest Avenue and Horner Avenue.

**Two Week Look Ahead:**

- a. Construction of drainage related activities are started from 10/14/2019 and completed by 11/1/2019.
- b. Construction of concrete curb and sidewalk related activities will start from 11/04/2019.

**Biweekly Progress Meeting:**

- a. Biweekly Progress Meeting No. 4 was held at Pennsauken Township building.

Susan Shin-Angulo  
Freeholder Liaison

2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988

John Wolick  
Director

[highway@camdencounty.com](mailto:highway@camdencounty.com)



Figure 1: Existing Type B inlet along Hollinshead Avenue West was Reconstructed using new casting, And Curb piece, Type N ECO was installed.



Figure 2: Curb piece, Type N ECO were installed for three inlets along Westfield Avenue, LT between Hillcrest Avenue and Hollinshead Avenue.



Figure 3: 15" Reinforced Concrete Pipe, Class IV was installed across Horner Avenue, LT.



Figure 4: 15" Reinforced Concrete Pipe, Class IV was installed across Horner Avenue, LT.

Susan Shin-Angulo  
Freeholder Liaison

2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988

John Wolick  
Director

[highway@camdencounty.com](mailto:highway@camdencounty.com)



Figure 5: 15" Reinforced Concrete Pipe was installed from inlet along Westfield Avenue to East Inlet along Horner Avenue, LT.



Figure 6: 15" Reinforced Concrete Pipe was installed from inlet along Westfield Avenue to East Inlet along Horner Avenue, LT.



Figure 7: 24" Reinforced Concrete Pipe, Class IV was installed across Westfield Avenue at Hillcrest Avenue.



Figure 8: 24" Reinforced Concrete Pipe, Class IV was installed across Westfield Avenue at Hillcrest Avenue.

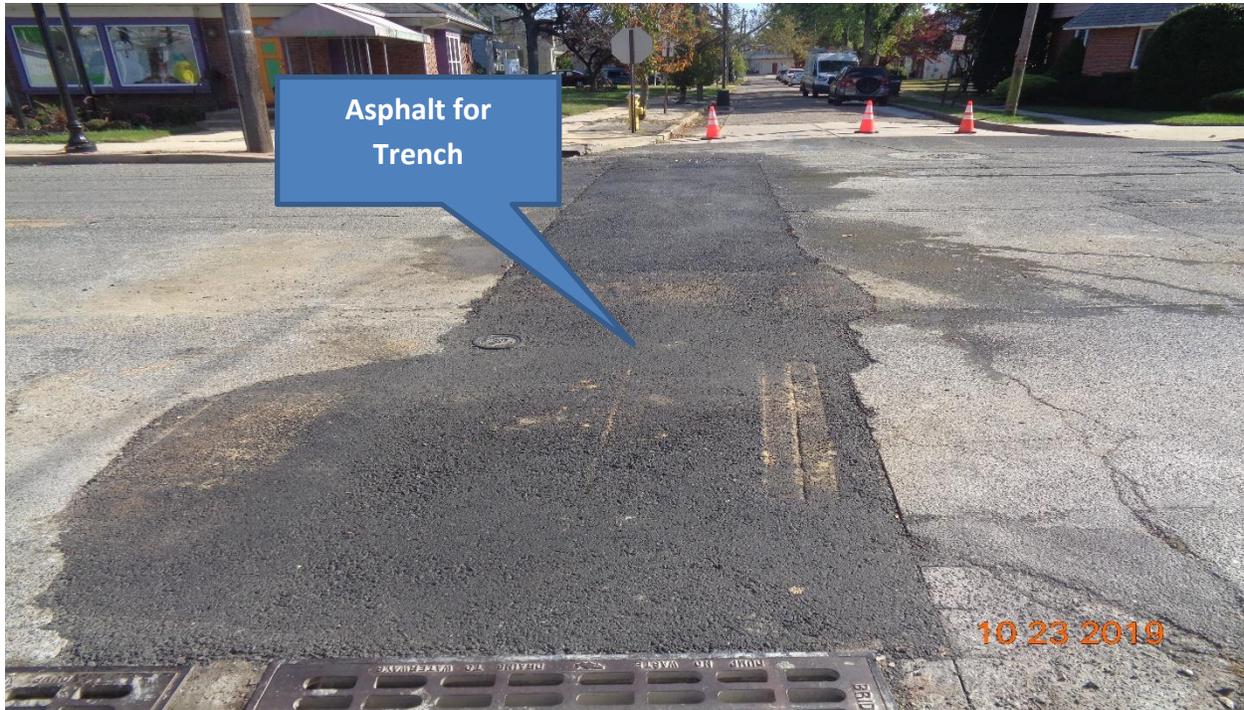


Figure 9: 24" Reinforced Concrete Pipe, Class IV was installed across Westfield Avenue at Hillcrest Avenue.




Figure 10: 18" Reinforced Concrete Pipe was installed along Westfield Avenue, LT Between Hillcrest Avenue and Horner Avenue

Susan Shin-Angulo  
Freeholder Liaison

2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988

John Wolick  
Director

[highway@camdencounty.com](mailto:highway@camdencounty.com)

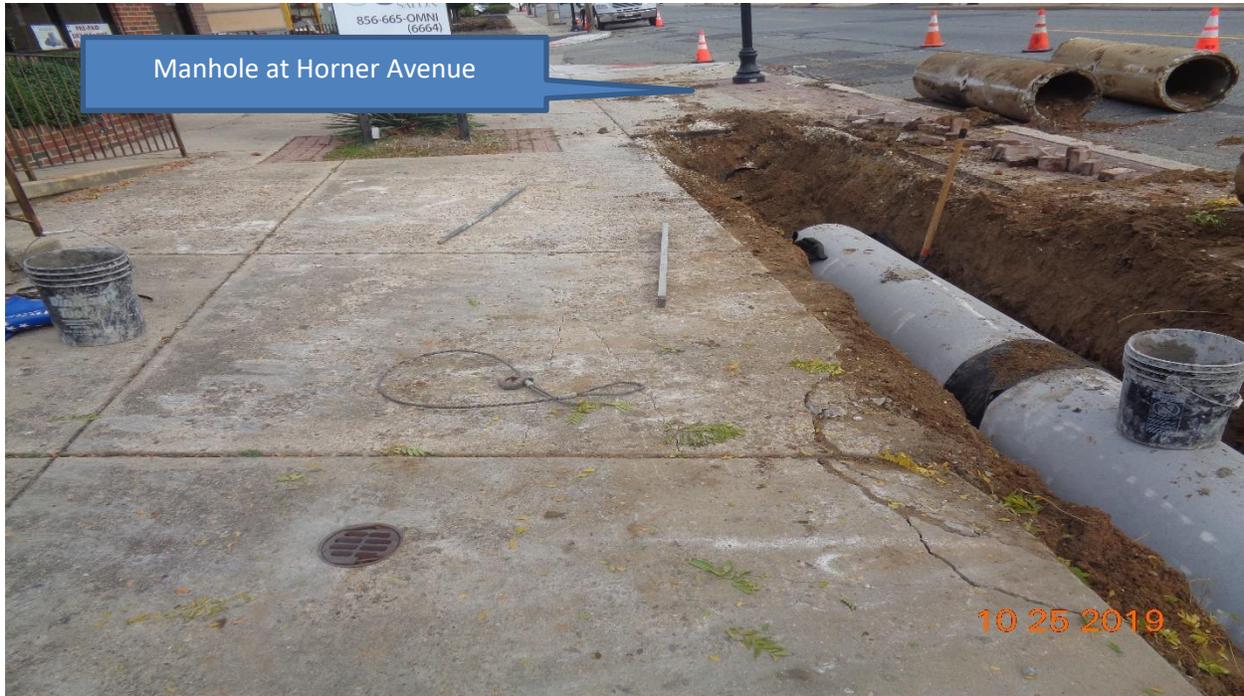

Manhole at Horner Avenue

10 25 2019

Figure 11: 18" Reinforced Concrete Pipe was installed along Westfield Avenue, LT Between Hillcrest Avenue and Horner Avenue



Asphalt for 7/Eleven  
Driveway –Entire  
Trench was backfilled

10 25 2019

Figure 11: 18" Reinforced Concrete Pipe was installed along Westfield Avenue, LT Between Hillcrest Avenue and Horner Avenue

Department of Public Works  
Complex

Susan Shin-Angulo  
Freeholder Liaison

John Wolick  
Director



Charles J. DePalma

2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988

[highway@camdencounty.com](mailto:highway@camdencounty.com)

Prepared By:  
Guvant Mistry  
Resident Engineer
