



IMPROVEMENTS TO WATSONTOWN-NEW FREEDOM ROAD (CR 691)
ERI Job # 30750 60
Boroughs of Berlin, Clementon, Lindenwold & Pine Hill
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #3
February 10, 2020 to February 14, 2020

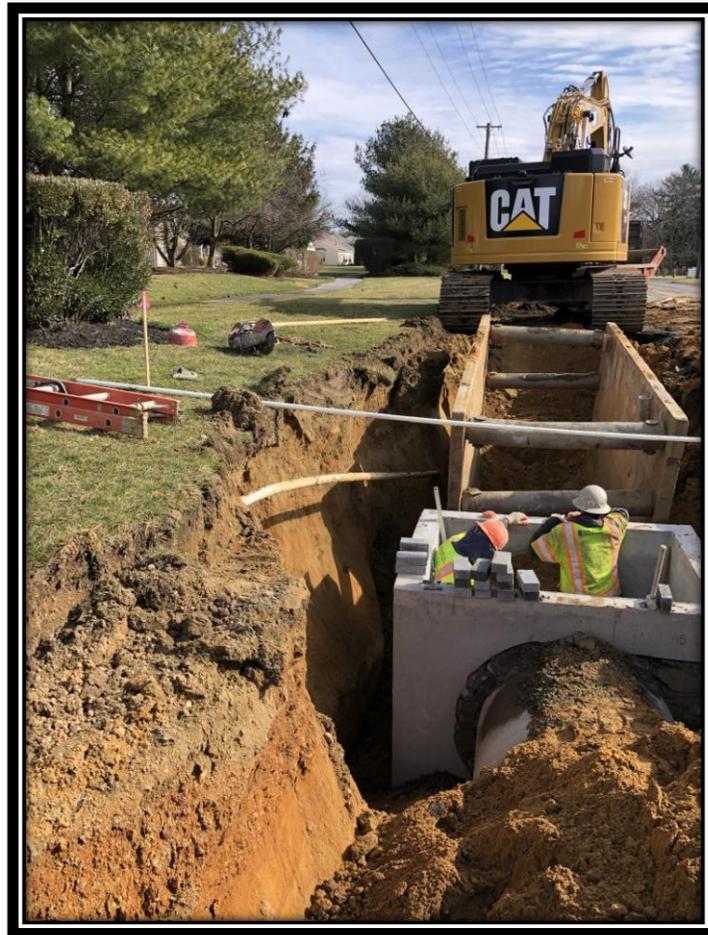


Figure: 1 – Installation of type B-2 inlet along the northbound lane of Watsonstown-New Freedom Road (CR 691) in the Borough of Berlin

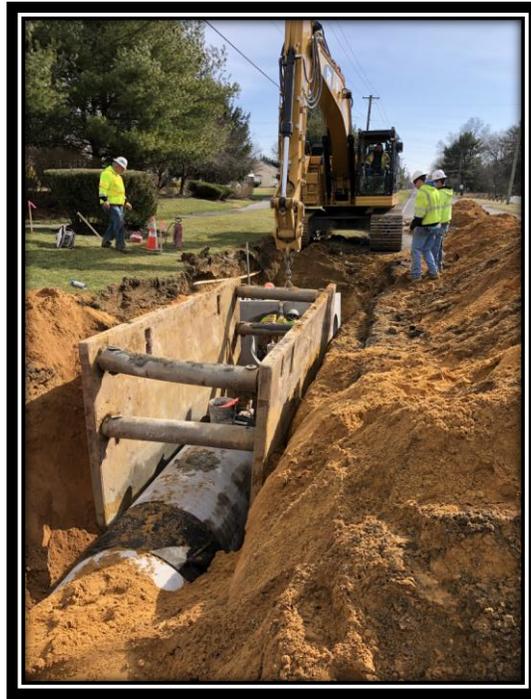


Figure: 2 – Installation of 36” RCP along the northbound lane of Watsontown-New Freedom Road (CR 691) in the Borough of Berlin



Figure: 3 – Restoration and compaction of the 36” RCP trench along the northbound lane of Watsontown-New Freedom Road (CR 691) in the Borough of Berlin

Work Completed the Week of February 10, 2020:

South State's pipe crew continued installation of storm sewer improvements along the northbound lane of Watstown-New Freedom Road between Carriage Stop Drive and Westbury Drive in the Borough of Berlin. The pipe crew then installed 31 linear feet of 18" RCP, 334 linear feet of 36" RCP and 1 type B-2 inlet.

#2: Police Uniform Law Enforcement Officer – 70 MH

#17: 18" RCP, Class V – 31 LF

#20: 36" RCP, Class V – 334 LF

#23: Inlet, Type B-2 – 1 Unit

Anticipated Work for the Week of February 17, 2020:

South State will continue installation of storm sewer improvements along the northbound lane between Carriage Stop Drive and Westbury Drive in the Borough of Berlin. South State will not work on February 17th due to the President's Day Holiday.

Notice to Proceed Date: January 13, 2020

Anticipated Completion Date: July 10, 2020

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
