



IMPROVEMENTS TO WATSONTOWN-NEW FREEDOM ROAD (CR 691)

ERI Job # 30750 60

Boroughs of Berlin, Clementon, Lindenwold & Pine Hill

County of Camden, New Jersey

WEEKLY PROGRESS REPORT #7

March 9, 2020 to March 13, 2020



Figure: 1 – Installation of type B inlet along the southbound lane of Watsontown-New Freedom Road (CR 691) in the Borough of Pine Hill



Figure: 2 – Installation of 6' diameter storm sewer manhole on Watsontown-New Freedom Road (CR 691) between Berlin-Clementon Road and Carriage Stop Drive in the Borough of Pine Hill

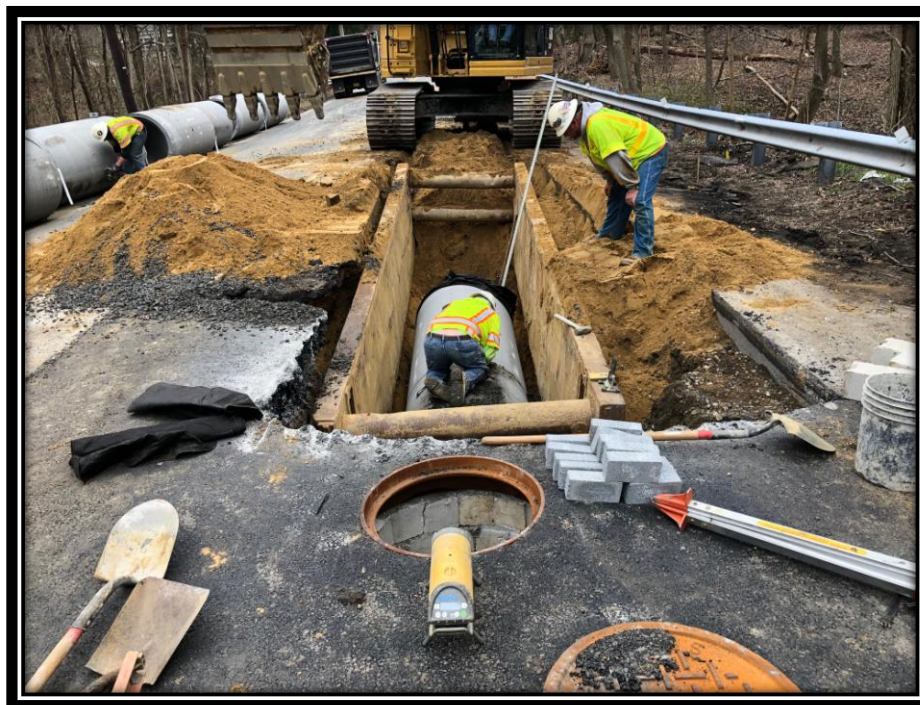


Figure: 3 – Installation of 36" RCP along the southbound lane of Watsontown-New Freedom Road (CR 691) between Berlin-Clementon Road and Carriage Stop Drive in the Borough of Pine Hill

Work Completed the Week of March 2, 2020:

South State's pipe crew completed the installation of storm sewer trunk line along the northbound lane of Watsontown-New Freedom Road between Westbury Drive and Wyndam Road in the Borough of Berlin. The pipe crew then began installation of the remaining storm sewer improvements along the southbound lane in the Borough of Pine Hill between Berlin Clementon Road and Carriage Stop Drive. The pipe crew installed 94 linear feet of 18" RCP, 104 linear feet of 36" RCP, 1 6' diameter storm sewer manhole and 3 type B inlets. South State then restored the pipe trench with HMA base course.

#2: Police Uniform Law Enforcement Officer – 78 MH

#17: 18" RCP, Class V – 94 LF

#20: 36" RCP, Class V – 104 LF

#22: Inlet, Type B – 3 Units

#26: Manhole, 6' Diameter – 1 Unit

Anticipated Work for the Week of March 13, 2020:

South State will continue the installation of the storm sewer improvements along the southbound lane between Clementon-Berlin Road and Carriage Stop Drive.

Notice to Proceed Date: January 13, 2020

Anticipated Completion Date: July 10, 2020

Prepared By:

A handwritten signature in blue ink, appearing to read 'C. J. Noll'.

C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
