



IMPROVEMENTS TO WATSONTOWN-NEW FREEDOM ROAD (CR 691)
ERI Job # 30750 60
Boroughs of Berlin, Clementon, Lindenwold & Pine Hill
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #6
March 2, 2020 to March 6, 2020



Figure: 1 – Installation of type B inlet along the southbound lane of Watsonstown-New Freedom Road (CR 691) in the Borough of Pine Hill

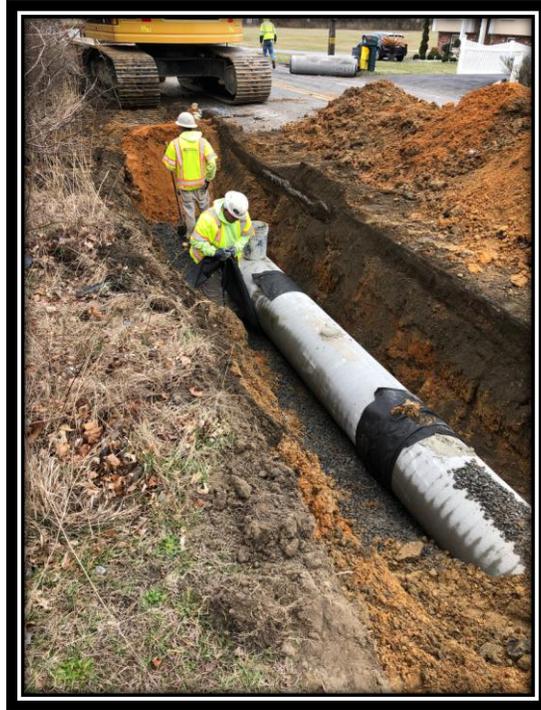


Figure: 2 – Installation of 18” RCP on Watsontown-New Freedom Road (CR 691) between Westbury Drive and Wyndam Road in the Borough of Berlin



Figure: 3 – Backfill and compaction of the 18” RCP trench along the northbound lane of Watsontown-New Freedom Road (CR 691) in the Borough of Berlin

Work Completed the Week of March 2, 2020:

South State's pipe crew continued installation of storm sewer improvements along the northbound lane of Watsonstown-New Freedom Road between Westbury Drive and Wyndam Road in the Borough of Berlin. The pipe crew installed 531 linear feet of 18" RCP, 1 6' diameter storm sewer manhole and 3 type B inlets. South State then restored the pipe trench with HMA base course.

#2: Police Uniform Law Enforcement Officer – 72 MH

#17: 18" RCP, Class V – 531 LF

#22: Inlet, Type B – 3 Units

#26: Manhole, 6' Diameter – 1 Unit

Anticipated Work for the Week of March 9, 2020:

South State will complete the installation of storm sewer improvements along the northbound lane between Westbury Drive and Wyndam Road in the Borough of Berlin. South State will then begin installation of the storm sewer improvements along the southbound lane between Clementon-Berlin Road and Carriage Stop Drive.

Notice to Proceed Date: January 13, 2020

Anticipated Completion Date: July 10, 2020

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
