camden county
Making It Better, Together.

CME ASSOCIATES

JOHN H. ALLGAIR, PE, PP, LS (1983-2001)
DAVID J. SAMUEL, PE, PP, CME
JOHN J. STEFANI, PE, LS, PP, CME
JAY B. CORNELL, PE, PP, CME
MICHAEL J. McCLELLAND, PE, PP, CME
GREGORY R. VALESI, PE, PP, CME

TIMOTHY W. GILLEN, PE, PP, CME
BRUCE M. KOCH, PE, PP, CME
LOUIS J. PLOSKONKA, PE, CME
TREVOR J. TAYLOR, PE, PP, CME
BEHRAM TURAN, PE, LSRP
LAURA J. NEUMANN, PE, PP
DOUGLAS ROHMEYER, PE, CFM, CME
ROBERT J. RUSSO, PE, PP, CME

Weekly Status Report – October 31, 2016 to November 4, 2016

Haddon Avenue Transit Village Roadway Improvements – Phase II

The Haddon Avenue Transit Village Roadway Improvements – Phase II Project was awarded to Jersey Construction, in the amount of $4,234,075.58. Change Order No. 1 results in an increase of $332,811.41 to the original contract amount of $4,234,075.58 to an adjusted contract amount of $4,566,886.99, for a 7.29% increase. The change order is a result of regulated material that was excavated and required disposal at an approved facility. The limits of the regulated material includes all excavation for the entire project length. Please see the following status breakdown for the various components involved in this project.

Roadway Reconstruction

- The contractor excavated an area of poor subgrade material and installed 12” Dense Graded Aggregate along the South Side of Haddon Avenue.

Electrical Improvements

- The contractor installed a fiber optic modem, emergency pre-emption system, uninterrupted power supply (UPS) system, ground wire #8 AWG, controller 8 phase, advanced push button, advanced pedestrian controller, traffic signal head, traffic signal mast arm aluminum, traffic signal standard aluminum, traffic signal cable 2 conductor, traffic signal cable 5 conductor, traffic signal cable 10 conductor, and fiber optic patch panel at the intersection of Haddon Avenue and Copewood Street.
- The contractor installed foundation lighting and a black meter cabinet at the intersection of Haddon Avenue and Vesper Boulevard.

Streetscaping Improvements

- The contractor installed stone pillars, decorative aluminum fence 4’, brick paver sidewalk, and structural soil along the South side of Haddon Avenue.

CONSULTING AND MUNICIPAL ENGINEERS
ONE MARKET STREET, SUITE 1F • CAMDEN, NEW JERSEY 08102 • (732) 410-2651

Figure 1 – Installation of decorative aluminum fence along South Side of Haddon Avenue.

Figure 2 – Installation of black meter cabinet at the intersection of Vesper Boulevard and Haddon Avenue.

Figure 3 – Installation of black meter cabinet and electrical conduit at the intersection of Vesper Boulevard and Haddon Avenue.

Figure 4 – Installation of decorative aluminum fence along South Side of Haddon Avenue.

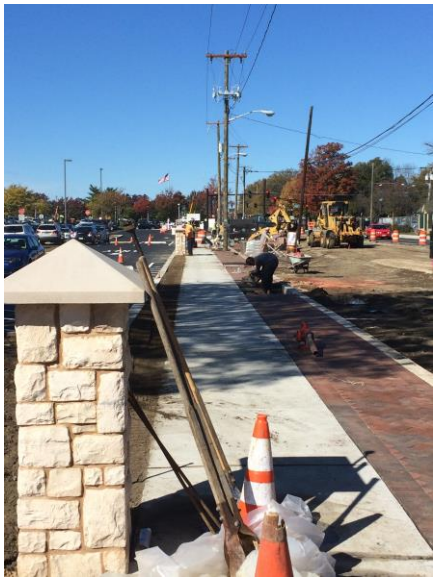

Storm Sewer

- No work for this portion of the project has been completed this week.

Shop Drawing Submittals

- No work for this portion of the project has been completed this week.

Utility Pole Relocation

- PSE&G and Comcast cable continued relocating utility poles and equipment.

Sanitary Sewer

- No work for this portion of the project has been completed this week.

Water Main

- The contractor installed a new fire hydrant along the South Side of Haddon Avenue.

Traffic Control Installation

- The South side of Haddon Avenue was shut down and traffic control was set up per the approved traffic control plan.

Changes to the Initial Contract Items

- No changes were made to the initial contract items this week.

NJDOT Comments

- No comments were received from NJDOT this week.

Environmental Remarks

- No environmental remarks were made this week.

Notice to Proceed Date: April 15, 2016
Contractor's Schedule Completion Date: December 25, 2016
Contract Completion Date: January 24, 2017
