Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director

camden county
Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Bid Number B1-21: Centre Street (CR 622) Roadway Improvements

From Locust Street to Cove Road (CR 616)

Borough of Merchantville and Pennsauken Township, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2018_Camden County – 00111

Progress Report #5

Week Ending June 18, 2021

Progress Photographs:

Photograph 1 – Driveway apron replacement on Centre Street continues between Rogers Avenue and Cedar Avenue.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director

camden county

Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Photograph 2 – Driveway apron replacement continues between Rogers Avenue and Cedar Avenue.

Photograph 3 – Preparing for concrete slab replacement at the Grant Avenue and Centre Street intersection.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director

camden county

Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Photograph 4 – Class V concrete pour for the slab replacement at the rant Avenue and Centre Street intersection.

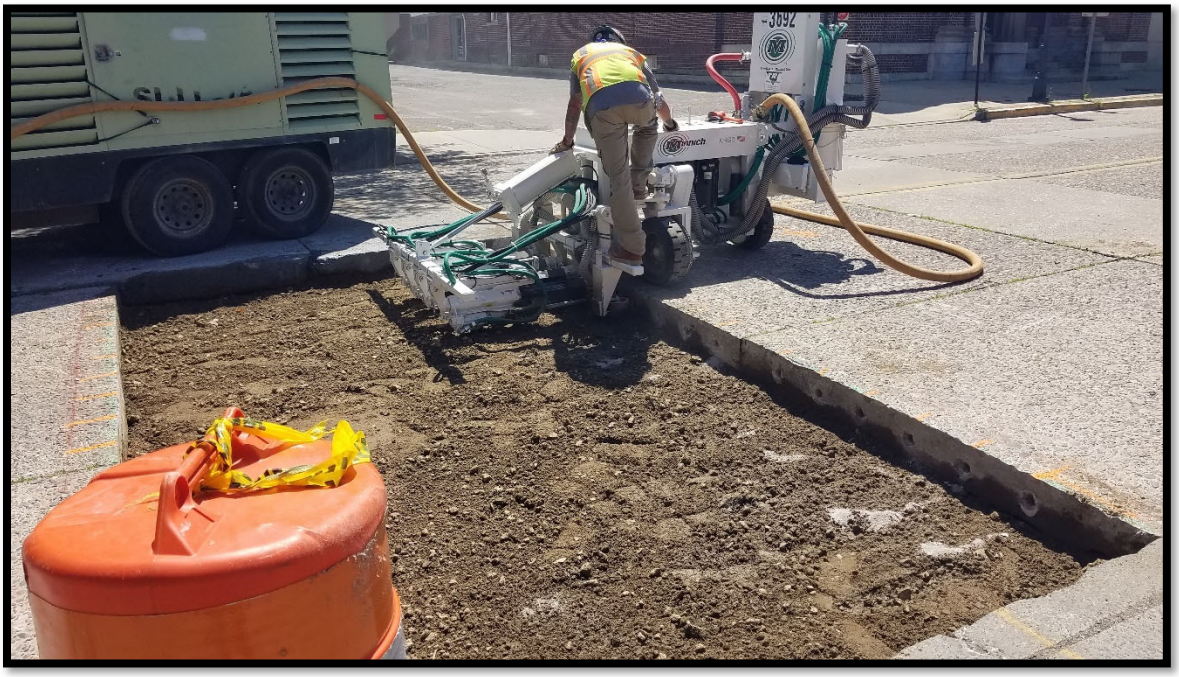

Photograph 5 – Dowel drilling in progress in preparation of slab replacement.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director

camden county

Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

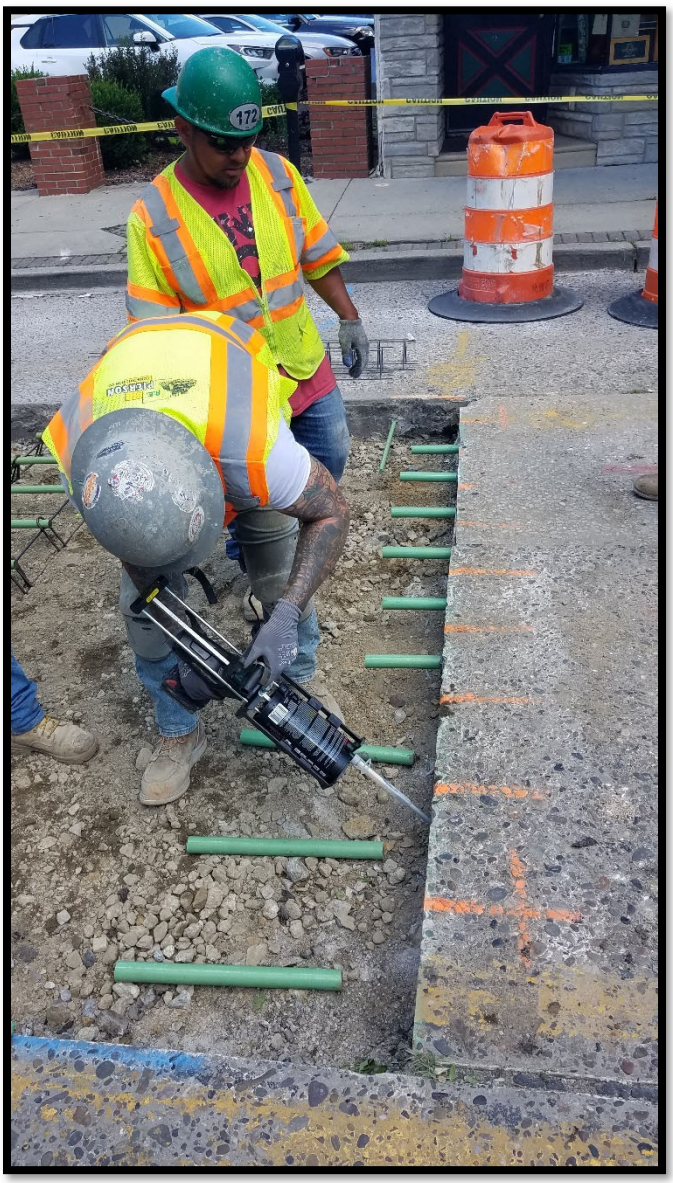

Photograph 6 – Dowels being installed in preparation of concrete slab replacement.

Photograph 7 – Dowels, expansion material and welded wire fabric installed in preparation of concrete slab replacement.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director

camden county

Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Photograph 8 – Reinforced concrete storm pipe being installed along Chestnut Avenue.

Photograph 9 – Storm inlets being installed along Chestnut Street.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director

camden county

Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Photograph 5 – Backfilling around new inlet on Chestnut Street.

Work Completed this Report Cycle:

- Contractor completed curb/gutter and flatwork along Centre Street between Rogers Avenue and Cedar Avenue.

- The Contractor prepared and poured concrete roadway sections between Park Avenue and Chestnut Avenue.

- The pipe crew installed 12" RCP storm pipe across Chestnut Avenue and built the type 'A' and type 'B' inlets at either end of the run.

Changes to the Initial Contract items:

- No change orders to date. A Requests For Information (RFI #002) approved quantity changes for the addition of new inlets and reduction in reconstructed inlets. Quantities will be adjusted in a future change order.

- A negotiated price for RFI #003 regarding gutter width exceeding 24” as indicated in the Contract Documents was forwarded to the County Engineer for approval. The County Engineer has requested that the cost proposal be revised to include total cost for widen gutter as supplemental items and not the cost of just the additional width. The cost deduction for existing items and the additional cost for Supplemental Pay Items will be incorporated into the Contract as an interim Change Order.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director

camden county
Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

- The longitudinal cracking in the concrete roadway subbase between the Merchantville/Pennsauken border and Cove Road was reviewed by Bach Associates and the County. Slabs to be removed and replaced were field located.

Project Schedule:

- The Notice to Proceed was issued with a start date of Monday, May 10, 2021.The date for Substantial Completion is Monday, December 6, 2021 and the date of Final Completion is Saturday, January 15, 2022.

- 15.6% of time used to date

- 0.0% paid to date. Payment Application #1 in the amount of $197,785.43 was submitted to the County Engineer on June 18, 2021. The Total Amount Estimated to date is $197,785.43, or 10.26% of the Contract Value of $1,928,469.75.

Prepared by: Mark R. Basehore, Jr., PE, CME
Bach Associates, PC
