Camden County Department of Public Works

Division of Engineering

Roadway and Drainage Improvements

Along Peter Cheeseman Road (CR 759)

Hickstown Road (CR 688) to Erial Road (CR 706)

Gloucester Township, Camden County, New Jersey

Weekly Progress Report # 3
June 29, 2020 to July 2, 2020

Figure 1
Trench box was needed to install 18"RCP round unforeseen Utilities in intersection

Figure 2
Unforeseen utilities found in intersection where new 18" RCP was installed

Figure 3
Compaction of drench through Intersection of College Dr. and Peter Cheeseman

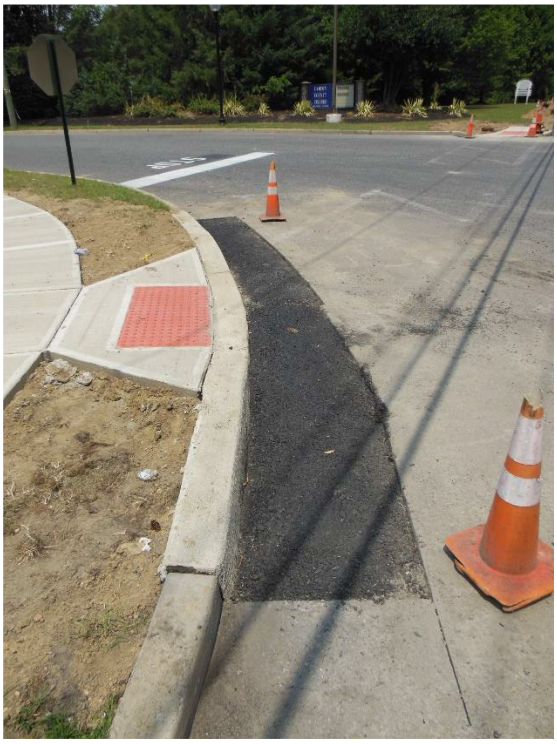

Figure 4
Placed asphalt in area that was removed to install ramp and curb

Figure 5
Contractor's staff checking to make sure DWS is correct while concrete is still workable

Figure 6
New curb forms ready to be poured

Work Completed Week of June 29, 2020:

- Completed 18" RCP
- Worked on Image detectors
- Started curb and sidewalk
- Layout of profile centerline has begun
- Inlet adjustments are taking place

Quantities Week of June 29, 2020:

- Item #3: Uniformed Police (68 MH)
- Item #10: Test Pits (1.0 CY)
- Item #11: Excavation, unclassified (11.0 CY)
- Item 12: DGA (176 SY)
- Item#22: 18" RCP (181 LF)
- Item #37: Concrete Sidewalk (150.2 SY)
- Item # 41: DWS (11 SY)
- Item # 42: Concrete Curb (218 LF)

Summary of Work Completed Week of June 29, 2020:

Contractor completed the installation of the 18" RCP. They are now working on curb and sidewalk. Inlet adjustments and centerline profile layout

Anticipated work for Week of June 29, 2020:

Curb and sidewalk work is being performed. Layout of profile line and electrical items work will continue.

Notice to Proceed Date:	Monday, June 15, 2020
Contract Completion Milestones	
Substantial Completion Date:	Sunday , September 13, 2020
Final Completion Date:	Tuesday, October 13, 2020
Accelerated Completion Date:	**Saturday, August 15, 2020**
Percent Complete by Duration:	**28% (are calculated to Accelerated Date)**
Percent Complete by Payments:	**15%**

Prepared By:
AECOM

Anthony Guerrieri
Project Manager
